

Install. Pos. (Leading Edge)

1717.631 m

Chainage Start

1709.720 m

Start Date

27/08/2024 01:39

Ring Type

U08

Chainage End

1708.125 m

Finish Date

27/08/2024 05:08

1) Operation Data

Advance Time

87 [min]

Ring Build Time

85 [min]

Downtime

37 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

6.297

8.800




Thrust force [kN]

73316

23323

75792




Contact Force (Articulation)

13085

10325

13582



TBM Advance Rate [mm/min]


Avg*

Min

Max

19

42




Face support pressure crown [bar]

1.8


1.6

2.0



Grout volume sum [m³]

13.9



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 386.3 [t]


Belt scale 2 173.5 [t]

Deviation (BS1/BS2) 223 [%]

Muck Volume

Theoretical 214.6 [m³]

Net Stroke 1597 [mm]

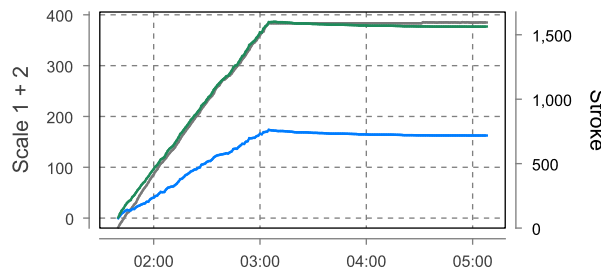

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 302 [L]

Polymer P003 0 [L]


Water Foam Unit 15,124 [L]

HD Polymer 160 [L]

Bentonite (1+2) 38,868 [L]

4) TBM Guidance System

H	V
Deviation Front	
-4	2 [mm]
Deviation Center	
-18	-13 [mm]
Deviation Rear	
-18	-13 [mm]

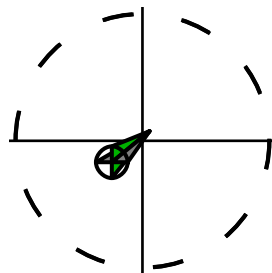

Roll	-3 mm/m	-0.1 °
Nick	8 mm/m	-1.0 °

Note: Value before Ring Build

5) Grouting

#8	[m³]	[bar]
A	2.3	5.3
B	0.1	0.03

#7	[m³]	[bar]
A	1.5	5.4
B	0.1	0.02

#6	[m³]	[bar]
A	2.4	4.3
B	0.2	5.6


#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

#1	[m³]	[bar]
A	2.3	4.8
B	0.2	6.1

#2	[m³]	[bar]
A	1.6	4.5
B	0.1	5.0

#3	[m³]	[bar]
A	2.8	4.1
B	0.2	5.8

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

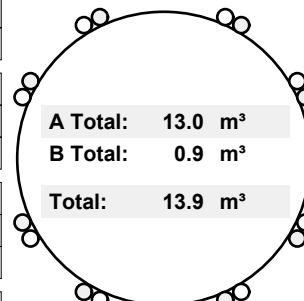

A Total: 13.0 m³

B Total: 0.9 m³

Total: 13.9 m³

Max. Volume [m³]

avg. Pressure [bar]

6) Segments

