

Install. Pos. (Leading Edge)

1712.829 m

Chainage Start

1704.916 m

Start Date

28/08/2024 01:26

Ring Type

U01

Chainage End

1703.322 m

Finish Date

28/08/2024 07:07

1) Operation Data

Advance Time

92 [min]

Ring Build Time

31 [min]

Downtime

216 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]


Avg*

Min

Max

3.717

5.187



TBM Advance Rate [mm/min]


Avg*

Min

Max

17

38




Thrust force [kN]

76234

20782

81872




Face support pressure crown [bar]

1.7

1.5

2.1




Contact Force (Articulation)

12556


10399

12910



Grout volume sum [m³]

14.0



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 413.9 [t]


Belt scale 2 121.9 [t]

Deviation (BS1/BS2) 340 [%]

Muck Volume

Theoretical 214.5 [m³]

Net Stroke 1596 [mm]

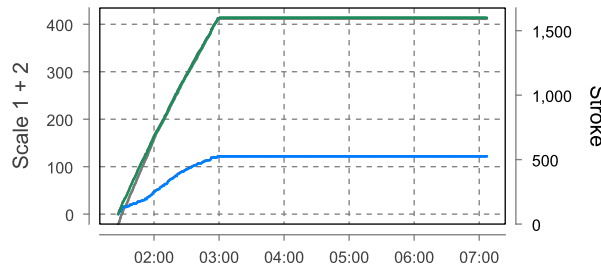

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 315 [L]

Polymer P003 0 [L]


Water Foam Unit 15,854 [L]

HD Polymer 106 [L]

Bentonite (1+2) 57,529 [L]

4) TBM Guidance System

H	V
Deviation Front	
13	5 [mm]
Deviation Center	
-6	-7 [mm]
Deviation Rear	
-6	-7 [mm]

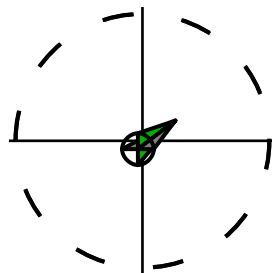

Roll	-0 mm/m	0.1 °
Nick	7 mm/m	-1.0 °

Note: Value before Ring Build

5) Grouting

#8	[m³]	[bar]
A	2.3	5.3
B	0.1	1.56

#7	[m³]	[bar]
A	1.7	4.8
B	0.1	1.03

#6	[m³]	[bar]
A	2.0	3.0
B	0.1	3.8


#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

#1	[m³]	[bar]
A	2.3	4.1
B	0.2	5.9

#2	[m³]	[bar]
A	2.2	4.6
B	0.1	6.4

#3	[m³]	[bar]
A	1.9	3.1
B	0.1	4.2

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

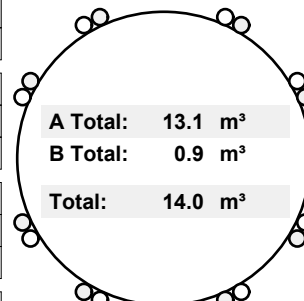

Max. Volume [m³]

avg. Pressure [bar]

6) Segments

