

Install. Pos. (Leading Edge)

1711.224 m

Chainage Start

1703.322 m

Start Date

28/08/2024 07:07

Ring Type

U10

Chainage End

1701.695 m

Finish Date

28/08/2024 11:54

1) Operation Data

Advance Time

117 [min]

Ring Build Time

52 [min]

Downtime

117 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

4.816

7.897


TBM Advance Rate [mm/min]


Avg*

Min

Max

19


38


Thrust force [kN]

75538

21908


82001


Face support pressure crown [bar]

1.8

1.5


2.1


Contact Force (Articulation)


13366

10864

14776


Grout volume sum [m³]

13.5


3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 452.4 [t]

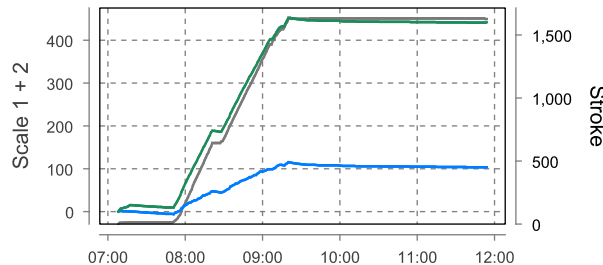
Belt scale 2 115.3 [t]

Deviation (BS1/BS2) 392 [%]

Muck Volume

Theoretical 219.3 [m³]

Net Stroke 1632 [mm]



Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 269 [L]

Polymer P003 0 [L]

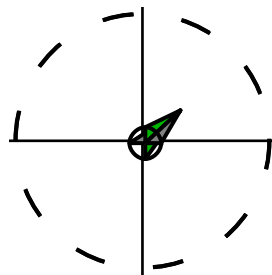
Water Foam Unit 13,598 [L]

HD Polymer 150 [L]

Bentonite (1+2) 51,044 [L]

4) TBM Guidance System

H	V
Deviation Front	
14	8 [mm]
Deviation Center	
-1	-5 [mm]
Deviation Rear	
-1	-5 [mm]



Roll	-2 mm/m	0.0 °
Nick	8 mm/m	-1.0 °

Note: Value before Ring Build

5) Grouting

#8	[m³]	[bar]
A	2.5	3.6
B	0.1	0.89

#7	[m³]	[bar]
A	1.9	4.3
B	0.1	1.44

#6	[m³]	[bar]
A	2.0	2.8
B	0.1	4.0

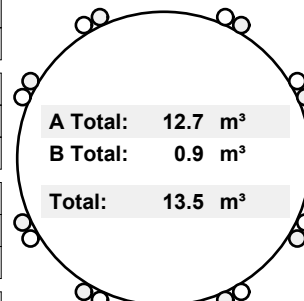
#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

#1	[m³]	[bar]
A	2.1	4.0
B	0.1	5.5

#2	[m³]	[bar]
A	1.7	4.2
B	0.1	5.3

#3	[m³]	[bar]
A	2.2	3.4
B	0.2	4.7

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0



A Total: 12.7 m³

B Total: 0.9 m³

Total: 13.5 m³

Max. Volume [m³]

avg. Pressure [bar]

6) Segments
