

Install. Pos. (Leading Edge)

1709.621 m

Chainage Start

1701.695 m

Start Date

28/08/2024 11:54

Ring Type

U03

Chainage End

1700.101 m

Finish Date

28/08/2024 16:08

1) Operation Data

Advance Time

98 [min]

Ring Build Time

57 [min]

Downtime

101 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

7.389

11.875



TBM Advance Rate [mm/min]


Avg*

Min

Max

19

40




Thrust force [kN]

74038

22487

78205




Face support pressure crown [bar]

1.8

1.6

2.0




Contact Force (Articulation)

13970


10559

15417



Grout volume sum [m³]

15.4



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 434.4 [t]


Belt scale 2 91.8 [t]

Deviation (BS1/BS2) 473 [%]

Muck Volume

Theoretical 214.5 [m³]

Net Stroke 1597 [mm]

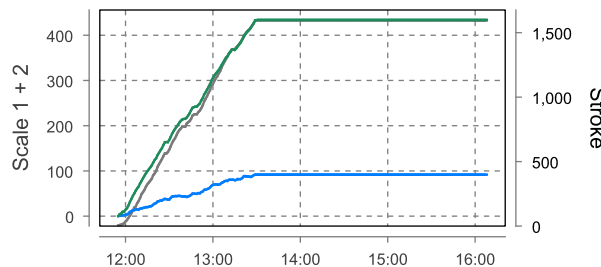

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 252 [L]

Polymer P003 0 [L]


Water Foam Unit 12,697 [L]

HD Polymer 141 [L]

Bentonite (1+2) 48,660 [L]

4) TBM Guidance System

H	V
Deviation Front	
13	13 [mm]
Deviation Center	
2	-2 [mm]
Deviation Rear	
2	-2 [mm]

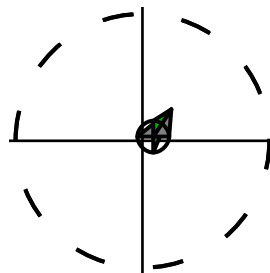

Roll	-2 mm/m	0.0 °
Nick	7 mm/m	-1.0 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.6	2.9
B	0.1	0.57

#7	[m³]	[bar]
A	2.1	4.1
B	0.1	1.38

#6	[m³]	[bar]
A	2.4	3.2
B	0.2	4.6

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

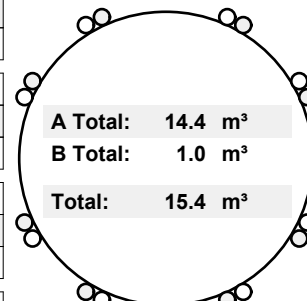

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.1	3.2
B	0.1	4.8

#2	[m³]	[bar]
A	2.0	3.2
B	0.1	4.4

#3	[m³]	[bar]
A	3.0	3.3
B	0.2	5.3

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

