

Install. Pos. (Leading Edge)

1708.016 m

Chainage Start

1700.101 m

Start Date

28/08/2024 16:08

Ring Type

U12

Chainage End

1698.475 m

Finish Date

28/08/2024 18:51

1) Operation Data

Advance Time

93 [min]

Ring Build Time

59 [min]

Downtime

10 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

8.754

12.066


TBM Advance Rate [mm/min]


Avg*

Min

Max

17


34


Thrust force [kN]

69065

21039


78141


Face support pressure crown [bar]

1.7

1.6


1.9


Contact Force (Articulation)


14705

10477

16177


Grout volume sum [m³]

13.8


3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 459.4 [t]

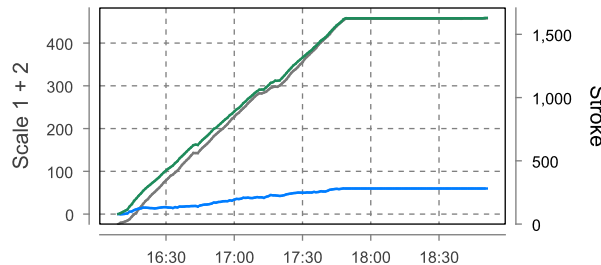
Belt scale 2 60.0 [t]

Deviation (BS1/BS2) 766 [%]

Muck Volume

Theoretical 218.6 [m³]

Net Stroke 1627 [mm]



Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 294 [L]

Polymer P003 0 [L]

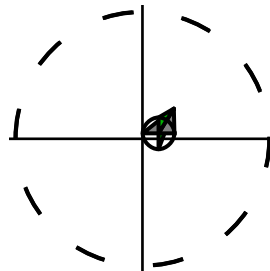
Water Foam Unit 14,773 [L]

HD Polymer 180 [L]

Bentonite (1+2) 53,250 [L]

4) TBM Guidance System

H	V
Deviation Front	
8	11 [mm]
Deviation Center	
3	1 [mm]
Deviation Rear	
3	1 [mm]



Roll	-1 mm/m	0.1 °
Nick	7 mm/m	-1.0 °

Note: Value before Ring Build

5) Grouting

#8	[m³]	[bar]
A	2.2	3.2
B	0.1	0.54

#7	[m³]	[bar]
A	1.8	3.7
B	0.1	1.48

#6	[m³]	[bar]
A	2.5	3.7
B	0.2	5.1

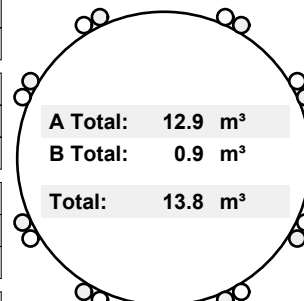
#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

#1	[m³]	[bar]
A	1.8	3.2
B	0.1	4.7

#2	[m³]	[bar]
A	1.7	3.6
B	0.1	4.9

#3	[m³]	[bar]
A	2.8	3.4
B	0.2	5.0

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0



A Total: 12.9 m³

B Total: 0.9 m³

Total: 13.8 m³

Max. Volume [m³]

avg. Pressure [bar]

6) Segments
