


Install. Pos. (Leading Edge)	1706.415 m	Chainage Start	1698.475 m	Start Date	28/08/2024 18:51
Ring Type	U11	Chainage End	1696.897 m	Finish Date	28/08/2024 21:52

1) Operation Data

Advance Time	91 [min]	Ring Build Time	26 [min]	Downtime	63 [min]
--------------	----------	-----------------	----------	----------	----------


2) Operation Data Diagrams

*Average Advance

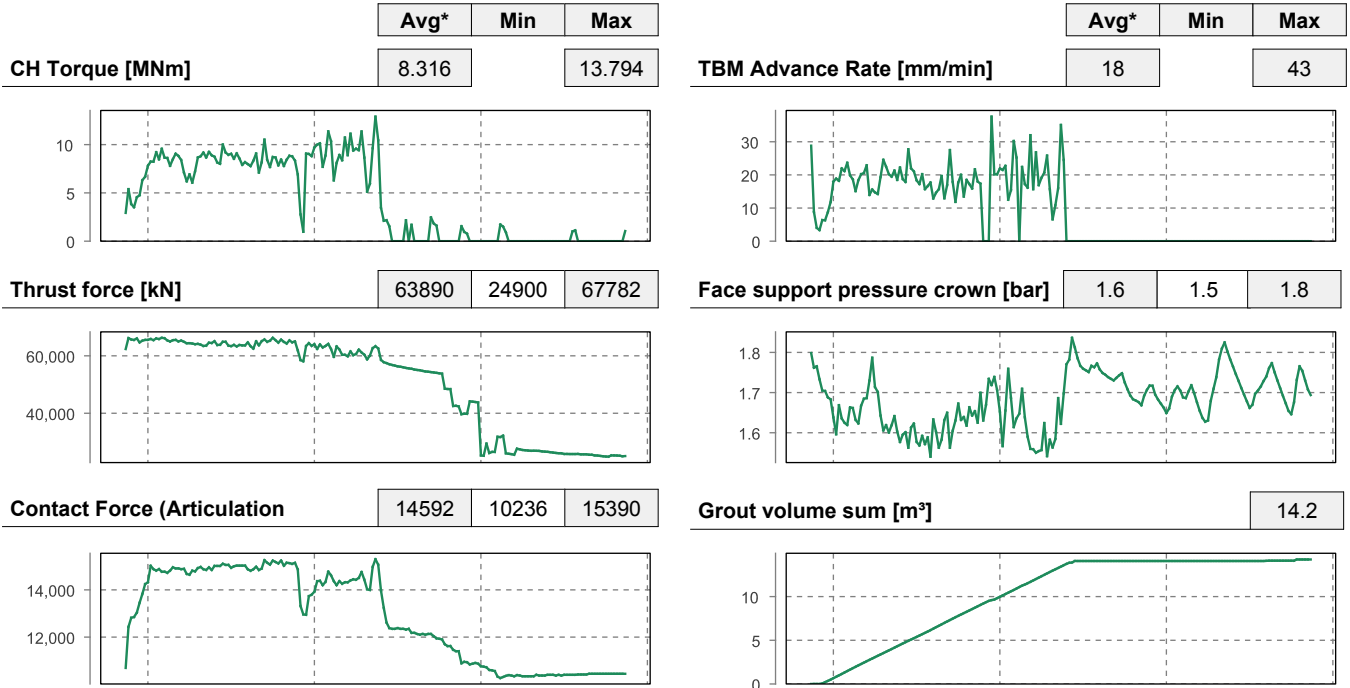

3) Muck Weight / Volume and Ground Conditioning


Excavated Weight	
Belt scale 1	403.1 [t]
Belt scale 2	39.8 [t]
Deviation (BS1/BS2)	1013 [%]
Muck Volume	
Theoretical	212.3 [m³]
Net Stroke	1580 [mm]

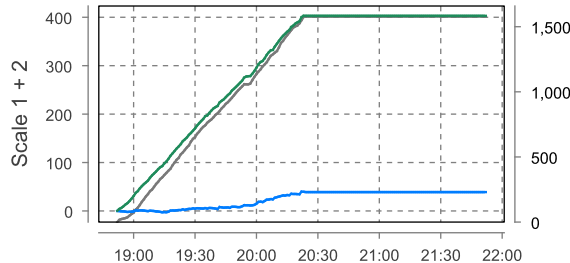

Ground Conditioning Volume	
Total Foam	100 [L]
Polymer P002	286 [L]
Polymer P003	0 [L]
Water Foam Unit	14,318 [L]
HD Polymer	134 [L]
Bentonite (1+2)	51,250 [L]

4) TBM Guidance System

H	V
Deviation Front	
1	12 [mm]
Deviation Center	
8	3 [mm]
Deviation Rear	
8	3 [mm]

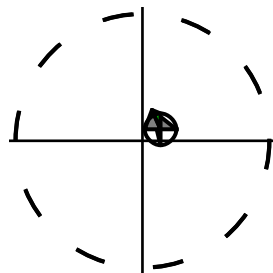

Roll	-2 mm/m	0.0 °
Nick	7 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.3	3.9
B	0.1	2.74

#7	[m³]	[bar]
A	2.0	4.9
B	0.1	3.06

#6	[m³]	[bar]
A	2.2	3.5
B	0.2	4.9

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

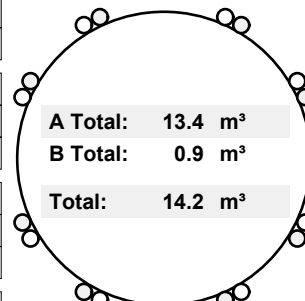

Max. Volume [m³]	
avg. Pressure [bar]	

#1	[m³]	[bar]
A	2.2	4.1
B	0.1	5.3

#2	[m³]	[bar]
A	1.9	4.3
B	0.1	5.1

#3	[m³]	[bar]
A	2.1	3.8
B	0.1	4.5

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

