

Install. Pos. (Leading Edge)

1704.811 m

Chainage Start

1696.897 m

Start Date

28/08/2024 21:52

Ring Type

U04

Chainage End

1695.309 m

Finish Date

29/08/2024 01:05

1) Operation Data

Advance Time

91 [min]

Ring Build Time

27 [min]

Downtime

73 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

8.324

11.850



TBM Advance Rate [mm/min]


Avg*

Min

Max

18

45




Thrust force [kN]

63353

21715

69841




Face support pressure crown [bar]

1.7

1.4

1.9




Contact Force (Articulation)

14571


10416

15621



Grout volume sum [m³]

14.1



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 483.3 [t]


Belt scale 2 103.5 [t]

Deviation (BS1/BS2) 467 [%]

Muck Volume

Theoretical 213.6 [m³]

Net Stroke 1589 [mm]

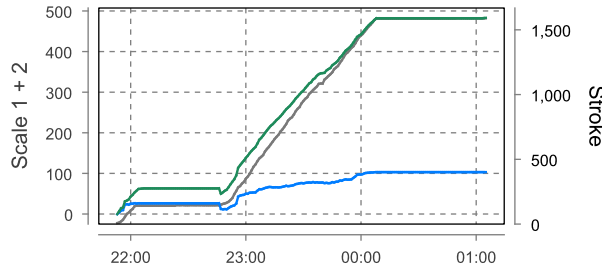

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 303 [L]

Polymer P003 0 [L]


Water Foam Unit 15,198 [L]

HD Polymer 438 [L]

Bentonite (1+2) 58,918 [L]

4) TBM Guidance System

H	V
Deviation Front	
-3	11 [mm]
Deviation Center	
7	4 [mm]
Deviation Rear	
7	4 [mm]

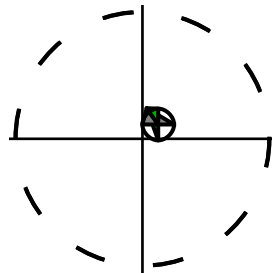

Roll	-2 mm/m	0.0 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.5	4.4
B	0.1	0.13

#7	[m³]	[bar]
A	1.8	4.4
B	0.1	1.83

#6	[m³]	[bar]
A	2.2	3.2
B	0.1	4.3

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

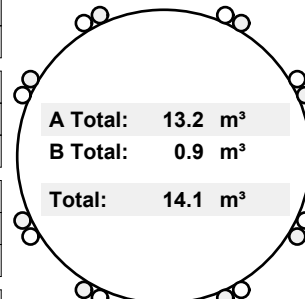

A Total: 13.2 m³

B Total: 0.9 m³

Total: 14.1 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.4	4.7
B	0.2	5.8

#2	[m³]	[bar]
A	2.0	4.0
B	0.1	4.7

#3	[m³]	[bar]
A	2.1	2.9
B	0.1	4.0

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

