


Install. Pos. (Leading Edge)	1701.609 m	Chainage Start	1693.696 m	Start Date	29/08/2024 04:10
Ring Type	U02	Chainage End	1692.089 m	Finish Date	29/08/2024 09:08

1) Operation Data

Advance Time	138 [min]	Ring Build Time	159 [min]	Downtime	0 [min]
--------------	-----------	-----------------	-----------	----------	---------


2) Operation Data Diagrams

*Average Advance

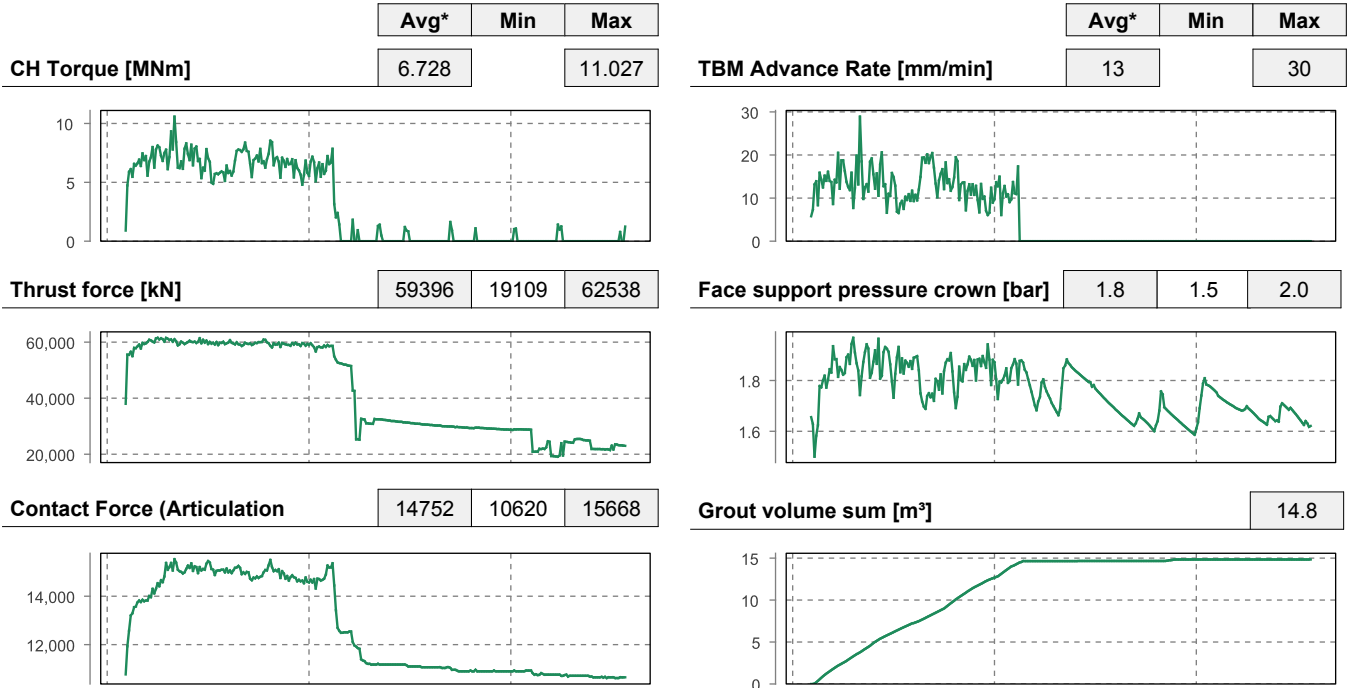

3) Muck Weight / Volume and Ground Conditioning


Excavated Weight	
Belt scale 1	528.3 [t]
Belt scale 2	50.8 [t]
Deviation (BS1/BS2)	1041 [%]
Muck Volume	
Theoretical	216.0 [m³]
Net Stroke	1608 [mm]

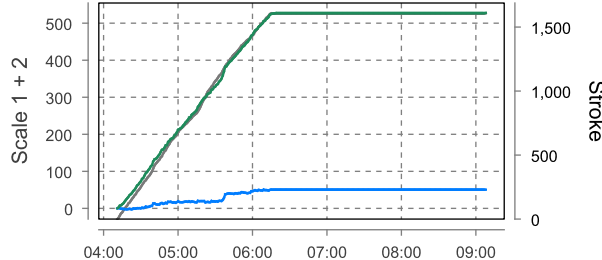

Ground Conditioning Volume	
Total Foam	100 [L]
Polymer P002	373 [L]
Polymer P003	0 [L]
Water Foam Unit	18,674 [L]
HD Polymer	221 [L]
Bentonite (1+2)	70,236 [L]

4) TBM Guidance System

H	V
Deviation Front	
-4	9 [mm]
Deviation Center	
1	7 [mm]
Deviation Rear	
1	7 [mm]

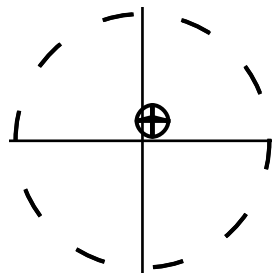

Roll	-1 mm/m	0.1 °
Nick	5 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.8	4.1
B	0.1	1.74

#7	[m³]	[bar]
A	1.3	3.4
B	0.1	2.82

#6	[m³]	[bar]
A	2.6	3.7
B	0.2	4.7

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

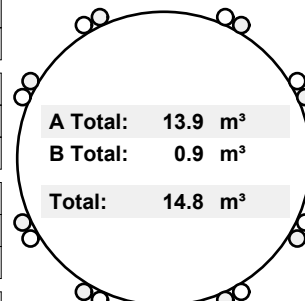

Max. Volume [m³]	
avg. Pressure [bar]	

#1	[m³]	[bar]
A	2.7	4.5
B	0.2	5.7

#2	[m³]	[bar]
A	2.1	4.2
B	0.1	4.7

#3	[m³]	[bar]
A	1.9	3.0
B	0.1	4.6

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

