

Install. Pos. (Leading Edge)

1700.006 m

Chainage Start

1692.089 m

Start Date

29/08/2024 09:08

Ring Type

U11

Chainage End

1690.479 m

Finish Date

29/08/2024 12:07

1) Operation Data

Advance Time

119 [min]

Ring Build Time

59 [min]

Downtime

0 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]


Avg*

Min

Max

6.844

10.549



TBM Advance Rate [mm/min]


Avg*

Min

Max

17

31




Thrust force [kN]

63969

23420

67428




Face support pressure crown [bar]

1.8

1.5

2.0




Contact Force (Articulation)

14699


10511

16245



Grout volume sum [m³]

13.8



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 480.2 [t]


Belt scale 2 117.6 [t]

Deviation (BS1/BS2) 408 [%]

Muck Volume

Theoretical 216.4 [m³]

Net Stroke 1610 [mm]

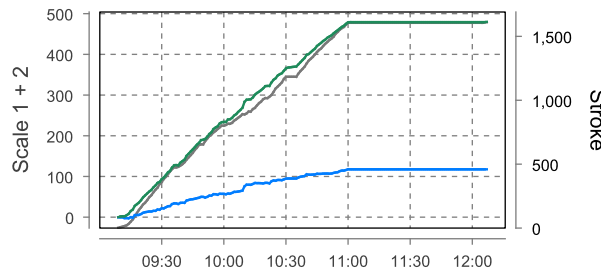

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 300 [L]

Polymer P003 0 [L]


Water Foam Unit 15,104 [L]

HD Polymer 380 [L]

Bentonite (1+2) 56,870 [L]

4) TBM Guidance System

H	V
Deviation Front	
-3	6 [mm]
Deviation Center	
2	5 [mm]
Deviation Rear	
2	5 [mm]

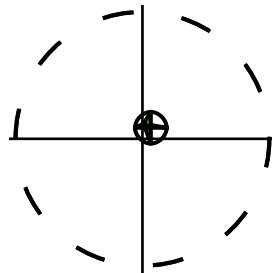

Roll	-3 mm/m	-0.0 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.3	3.3
B	0.1	1.41

#7	[m³]	[bar]
A	1.9	4.4
B	0.1	1.71

#6	[m³]	[bar]
A	2.4	3.4
B	0.2	4.7

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

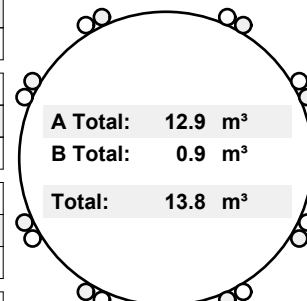

A Total: 12.9 m³

B Total: 0.9 m³

Total: 13.8 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.0	3.6
B	0.1	4.7

#2	[m³]	[bar]
A	1.8	3.9
B	0.1	4.6

#3	[m³]	[bar]
A	2.2	5.9
B	0.1	5.1

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

