

Install. Pos. (Leading Edge)

1696.803 m

Chainage Start

1688.881 m

Start Date

29/08/2024 17:41

Ring Type

U11

Chainage End

1687.291 m

Finish Date

29/08/2024 20:06

1) Operation Data

Advance Time

111 [min]

Ring Build Time

27 [min]

Downtime

5 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]


Avg*

Min

Max

6.371

11.156


TBM Advance Rate [mm/min]


Avg*

Min

Max

15


30


Thrust force [kN]

69753

26218


75406


Face support pressure crown [bar]

1.8

1.5


2.0


Contact Force (Articulation)


14785

10857

16744


Grout volume sum [m³]

12.9


3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 523.3 [t]

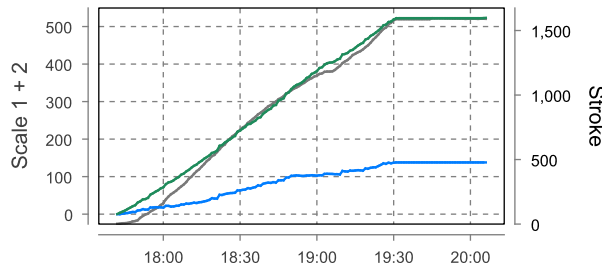
Belt scale 2 137.9 [t]

Deviation (BS1/BS2) 380 [%]

Muck Volume

Theoretical 214.3 [m³]

Net Stroke 1595 [mm]



Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 304 [L]

Polymer P003 0 [L]

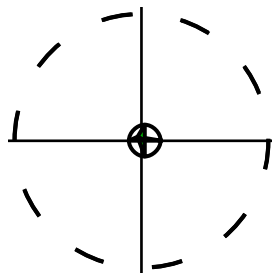
Water Foam Unit 15,231 [L]

HD Polymer 275 [L]

Bentonite (1+2) 59,378 [L]

4) TBM Guidance System

H	V
Deviation Front	
-7	-1 [mm]
Deviation Center	
1	-1 [mm]
Deviation Rear	
1	-1 [mm]



Roll	-2 mm/m	0.0 °
Nick	5 mm/m	-1.2 °

Note: Value before Ring Build

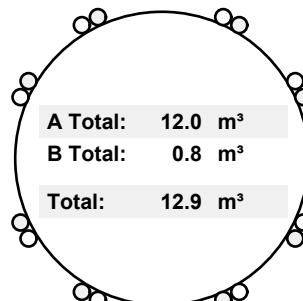
5) Grouting

#8	[m³]	[bar]
A	1.9	3.5
B	0.1	1.65

#7	[m³]	[bar]
A	1.4	3.8
B	0.1	2.53

#6	[m³]	[bar]
A	2.7	3.8
B	0.2	4.7

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0


A Total: 12.0 m³
B Total: 0.8 m³
Total: 12.9 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	1.9	3.5
B	0.1	4.7

#2	[m³]	[bar]
A	1.8	3.8
B	0.1	4.6

#3	[m³]	[bar]
A	2.1	3.5
B	0.1	4.6

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments
