

Install. Pos. (Leading Edge)

1693.595 m

Chainage Start

1685.685 m

Start Date

29/08/2024 22:22

Ring Type

U04

Chainage End

1684.089 m

Finish Date

30/08/2024 00:36

1) Operation Data

Advance Time

104 [min]

Ring Build Time

26 [min]

Downtime

0 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]


Avg*

Min

Max

8.033

12.715



TBM Advance Rate [mm/min]


Avg*

Min

Max

17

30




Thrust force [kN]

55885

23098

60254




Face support pressure crown [bar]

1.7

1.6

1.9




Contact Force (Articulation)

15480


10783

16642



Grout volume sum [m³]

14.1



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 497.7 [t]


Belt scale 2 153.5 [t]

Deviation (BS1/BS2) 324 [%]

Muck Volume

Theoretical 214.7 [m³]

Net Stroke 1598 [mm]

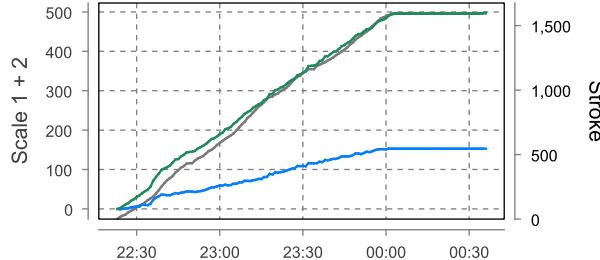

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 274 [L]

Polymer P003 0 [L]


Water Foam Unit 13,740 [L]

HD Polymer 217 [L]

Bentonite (1+2) 62,112 [L]

4) TBM Guidance System

H	V
Deviation Front	
0	1 [mm]
Deviation Center	
-1	-1 [mm]
Deviation Rear	
-1	-1 [mm]

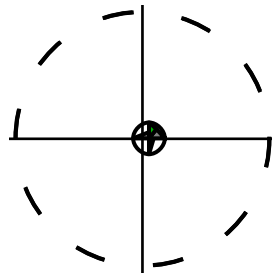

Roll	-4 mm/m	-0.1 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.5	4.4
B	0.1	2.21

#7	[m³]	[bar]
A	1.5	3.9
B	0.1	2.22

#6	[m³]	[bar]
A	2.3	3.1
B	0.2	3.9

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

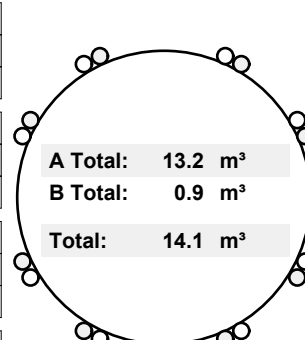

A Total: 13.2 m³

B Total: 0.9 m³

Total: 14.1 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.5	4.2
B	0.2	5.1

#2	[m³]	[bar]
A	1.7	3.4
B	0.1	4.4

#3	[m³]	[bar]
A	2.1	2.8
B	0.1	3.7

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

