


Install. Pos. (Leading Edge)	1690.393 m	Chainage Start	1682.489 m	Start Date	30/08/2024 03:58
Ring Type	U15	Chainage End	1680.870 m	Finish Date	30/08/2024 06:12

1) Operation Data

Advance Time	107 [min]	Ring Build Time	30 [min]	Downtime	1 [min]
--------------	-----------	-----------------	----------	----------	---------


2) Operation Data Diagrams

*Average Advance

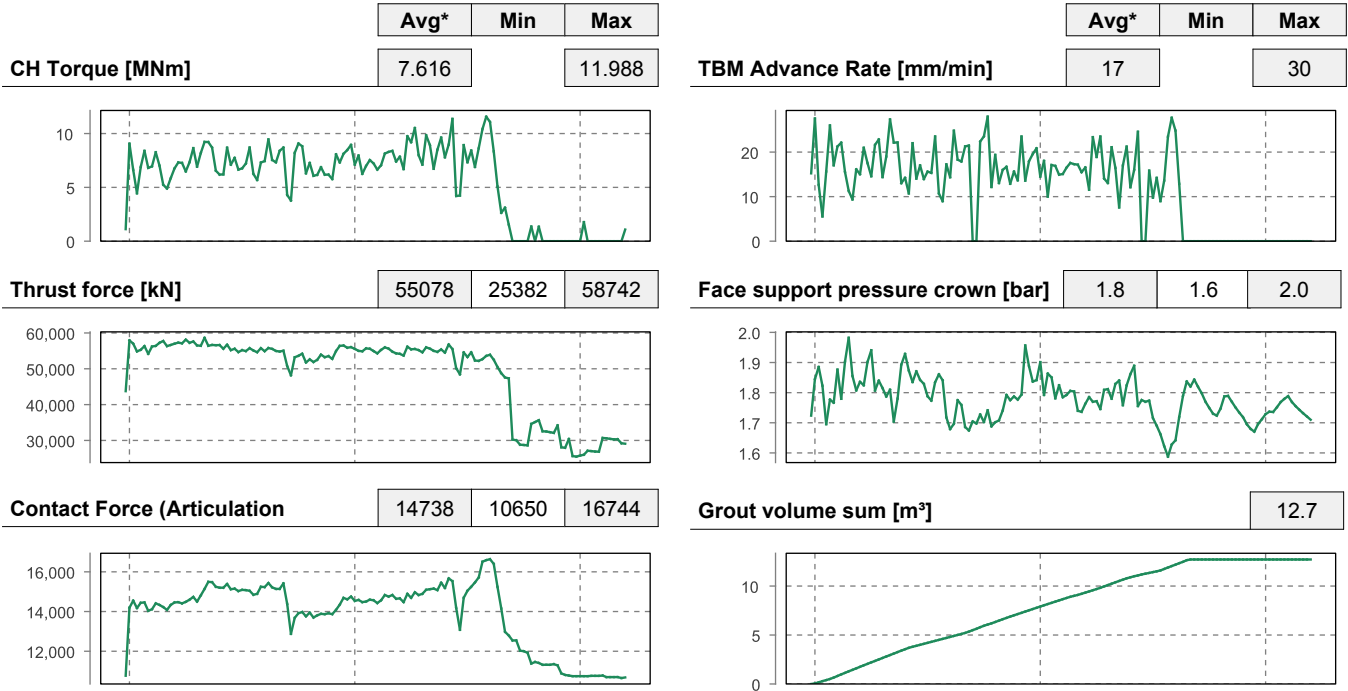

3) Muck Weight / Volume and Ground Conditioning


Excavated Weight	
Belt scale 1	503.8 [t]
Belt scale 2	102.0 [t]
Deviation (BS1/BS2)	494 [%]
Muck Volume	
Theoretical	217.6 [m³]
Net Stroke	1620 [mm]

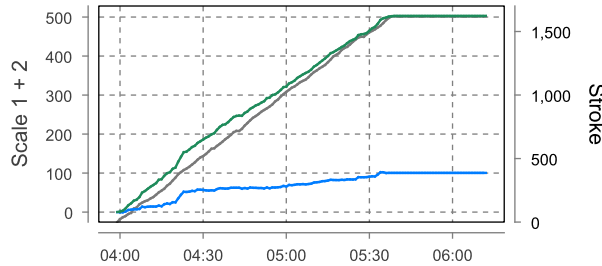

Ground Conditioning Volume	
Total Foam	100 [L]
Polymer P002	264 [L]
Polymer P003	0 [L]
Water Foam Unit	13,268 [L]
HD Polymer	187 [L]
Bentonite (1+2)	54,165 [L]

4) TBM Guidance System

H	V
Deviation Front	
-8	-0 [mm]
Deviation Center	
2	-4 [mm]
Deviation Rear	
2	-4 [mm]

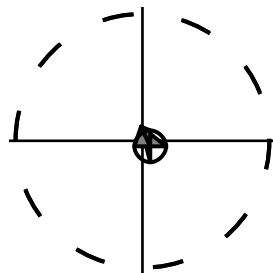

Roll	-4 mm/m	-0.1 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.3	4.4
B	0.1	1.73

#7	[m³]	[bar]
A	1.4	4.1
B	0.1	2.65

#6	[m³]	[bar]
A	2.2	3.4
B	0.2	4.5

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

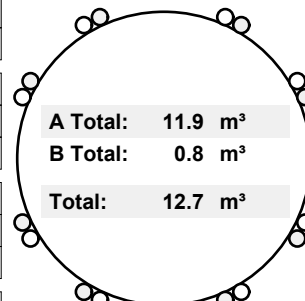

Max. Volume [m³]	
avg. Pressure [bar]	

#1	[m³]	[bar]
A	2.3	4.4
B	0.2	5.0

#2	[m³]	[bar]
A	1.6	3.8
B	0.1	4.4

#3	[m³]	[bar]
A	1.7	3.5
B	0.1	3.6

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

