

Install. Pos. (Leading Edge)

1688.792 m

Chainage Start

1680.870 m

Start Date

30/08/2024 06:12

Ring Type

U14

Chainage End

1679.284 m

Finish Date

30/08/2024 10:23

1) Operation Data

Advance Time

102 [min]

Ring Build Time

45 [min]

Downtime

103 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]

Avg*

Min

Max

8.270

14.463

TBM Advance Rate [mm/min]



Avg*

Min

Max

16

30


Thrust force [kN]

51482

20106



58292

Face support pressure crown [bar]

1.7

1.1

2.0


Contact Force (Articulation)



15678

10182

20093

Grout volume sum [m³]

12.4


3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 445.1 [t]

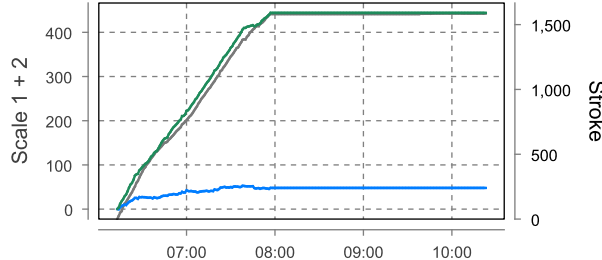
Belt scale 2 53.4 [t]

Deviation (BS1/BS2) 834 [%]

Muck Volume

Theoretical 213.3 [m³]

Net Stroke 1587 [mm]



Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 369 [L]

Polymer P003 0 [L]

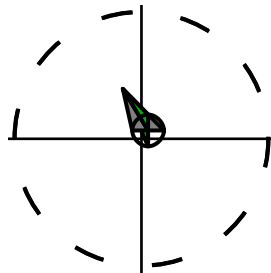
Water Foam Unit 18,595 [L]

HD Polymer 182 [L]

Bentonite (1+2) 70,447 [L]

4) TBM Guidance System

H	V
Deviation Front	
-12	6 [mm]
Deviation Center	
-0	-3 [mm]
Deviation Rear	
-0	-3 [mm]



Roll	-4 mm/m	-0.1 °
Nick	7 mm/m	-1.1 °

Note: Value before Ring Build

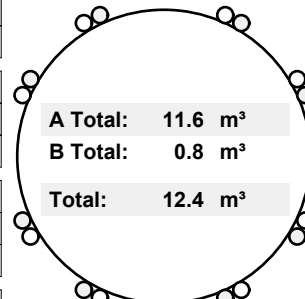
5) Grouting

#8	[m³]	[bar]
A	1.7	3.8
B	0.1	1.86

#7	[m³]	[bar]
A	1.7	4.2
B	0.1	1.94

#6	[m³]	[bar]
A	2.4	3.8
B	0.2	4.8

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0



Max. Volume [m³]
avg. Pressure [bar]

#1	[m³]	[bar]
A	2.0	4.0
B	0.1	4.6

#2	[m³]	[bar]
A	1.6	4.0
B	0.1	4.5

#3	[m³]	[bar]
A	1.9	4.2
B	0.1	4.4

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments
