

Install. Pos. (Leading Edge)

1685.587 m

Chainage Start

1677.667 m

Start Date

30/08/2024 13:47

Ring Type

U16

Chainage End

1676.054 m

Finish Date

30/08/2024 21:37

1) Operation Data

Advance Time

115 [min]

Ring Build Time

28 [min]

Downtime

326 [min]


2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]
Avg*
Min
Max


7.684

11.725


TBM Advance Rate [mm/min]
Avg*
Min
Max

16


29


Thrust force [kN]

58206

19463


61605


Face support pressure crown [bar]

1.8

1.6


2.0


Contact Force (Articulation)


15279

10186

17077


Grout volume sum [m³]

14.8


3) Muck Weight / Volume and Ground Conditioning
Excavated Weight

Belt scale 1 467.0 [t]

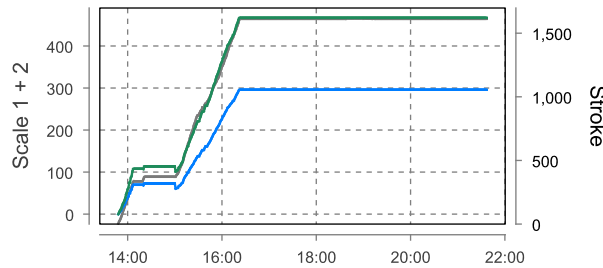
Belt scale 2 295.8 [t]

Deviation (BS1/BS2) 158 [%]

Muck Volume

Theoretical 217.3 [m³]

Net Stroke 1617 [mm]


Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 310 [L]

Polymer P003 0 [L]

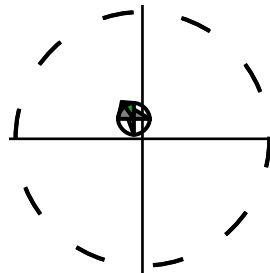
Water Foam Unit 15,778 [L]

HD Polymer 155 [L]

Bentonite (1+2) 69,334 [L]

4) TBM Guidance System

H	V
Deviation Front	
-18	16 [mm]
Deviation Center	
-5	7 [mm]
Deviation Rear	
-5	7 [mm]



Roll	-2 mm/m	0.1 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build

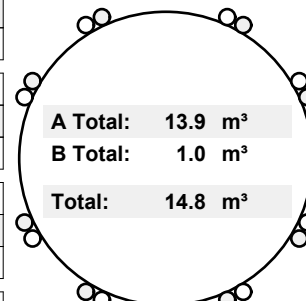
5) Grouting

#8	[m³]	[bar]
A	2.3	4.6
B	0.1	0.22

#7	[m³]	[bar]
A	2.1	5.5
B	0.1	2.67

#6	[m³]	[bar]
A	1.9	3.7
B	0.1	4.2

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0



Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.2	4.3
B	0.2	5.2

#2	[m³]	[bar]
A	2.0	4.7
B	0.1	5.6

#3	[m³]	[bar]
A	3.1	4.7
B	0.2	6.7

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments
