

Install. Pos. (Leading Edge)

1682.385 m

Chainage Start

1674.474 m

Start Date

30/08/2024 23:54

Ring Type

U16

Chainage End

1672.875 m

Finish Date

31/08/2024 02:32

1) Operation Data

Advance Time

115 [min]

Ring Build Time

32 [min]


Downtime

9 [min]


2) Operation Data Diagrams

*Average Advance


	Avg*	Min	Max
CH Torque [MNm]	7.881		12.716




	Avg*	Min	Max
TBM Advance Rate [mm/min]	14		29




Thrust force [kN]	64750	23002	68586
-------------------	-------	-------	-------




Face support pressure crown [bar]	1.7	1.5	1.9
-----------------------------------	-----	-----	-----



Contact Force (Articulation)	15453	10616	17005
------------------------------	-------	-------	-------




Grout volume sum [m³]	13.8
-----------------------	------



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight	
Belt scale 1	514.9 [t]
Belt scale 2	325.5 [t]
Deviation (BS1/BS2)	158 [%]

Muck Volume	
Theoretical	215.1 [m³]
Net Stroke	1601 [mm]

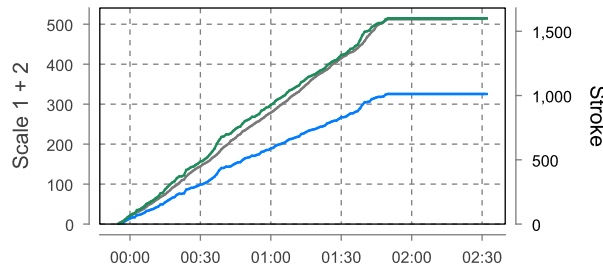


Ground Conditioning Volume	
Total Foam	100 [L]

Polymer P002	319 [L]
Polymer P003	0 [L]
Water Foam Unit	15,978 [L]
HD Polymer	123 [L]
Bentonite (1+2)	51,875 [L]

4) TBM Guidance System

H	V
Deviation Front	
-7	8 [mm]
Deviation Center	
-5	8 [mm]
Deviation Rear	
-5	8 [mm]

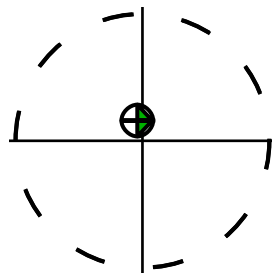

Roll	-2 mm/m	0.0 °
Nick	5 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.4	5.1
B	0.1	0.20

#7	[m³]	[bar]
A	1.7	4.6
B	0.1	2.78

#6	[m³]	[bar]
A	2.3	4.3
B	0.2	4.9

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

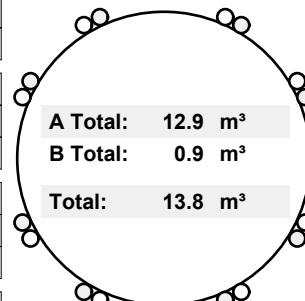

A Total: 12.9 m³

B Total: 0.9 m³

Total: 13.8 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.3	4.7
B	0.2	5.4

#2	[m³]	[bar]
A	1.6	5.0
B	0.1	4.7

#3	[m³]	[bar]
A	2.2	4.3
B	0.2	4.8

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

