

Install. Pos. (Leading Edge)

1680.785 m

Chainage Start

1672.875 m

Start Date

31/08/2024 02:32

Ring Type

U07

Chainage End

1671.277 m

Finish Date

31/08/2024 05:00

1) Operation Data

Advance Time

105 [min]

Ring Build Time

42 [min]

Downtime

0 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]


Avg*

Min

Max

8.357

12.108



TBM Advance Rate [mm/min]


Avg*

Min

Max

16

30




Thrust force [kN]

61673

20910

65048




Face support pressure crown [bar]

1.7

1.5

1.9




Contact Force (Articulation)

14928


10616

16238



Grout volume sum [m³]

13.4



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 458.1 [t]


Belt scale 2 280.4 [t]

Deviation (BS1/BS2) 163 [%]

Muck Volume

Theoretical 215.0 [m³]

Net Stroke 1600 [mm]

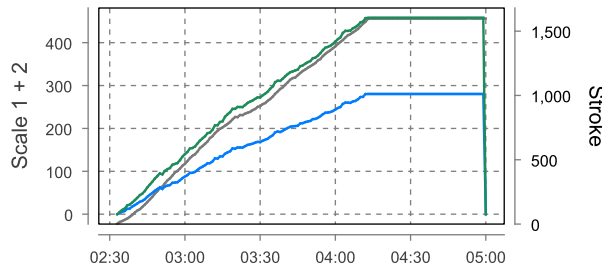

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 271 [L]

Polymer P003 0 [L]


Water Foam Unit 13,594 [L]

HD Polymer 124 [L]

Bentonite (1+2) 59,911 [L]

4) TBM Guidance System

H	V
Deviation Front	
-2	6 [mm]
Deviation Center	
-3	7 [mm]
Deviation Rear	
-3	7 [mm]

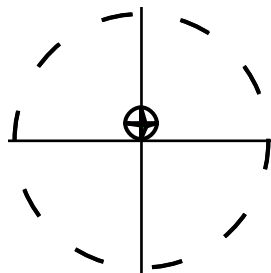

Roll	-3 mm/m	-0.1 °
Nick	5 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.1	5.3
B	0.1	1.23

#7	[m³]	[bar]
A	1.8	5.0
B	0.1	2.01

#6	[m³]	[bar]
A	2.3	3.9
B	0.2	4.5

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

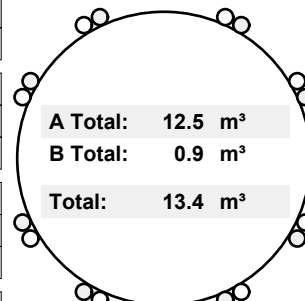

A Total: 12.5 m³

B Total: 0.9 m³

Total: 13.4 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.4	4.9
B	0.2	5.7

#2	[m³]	[bar]
A	1.8	5.0
B	0.1	5.1

#3	[m³]	[bar]
A	2.0	4.2
B	0.1	4.5

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

