

Install. Pos. (Leading Edge)

1679.176 m

Chainage Start

1671.277 m

Start Date

31/08/2024 05:00

Ring Type

U12

Chainage End

1669.664 m

Finish Date

31/08/2024 07:36

1) Operation Data

Advance Time

105 [min]

Ring Build Time

46 [min]

Downtime

0 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

8.707

12.175


TBM Advance Rate [mm/min]


Avg*

Min

Max

16


24


Thrust force [kN]

61636

20428


66495


Face support pressure crown [bar]

1.7

1.4


1.9


Contact Force (Articulation)


15390

9948

17541


Grout volume sum [m³]

13.6


3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 453.5 [t]

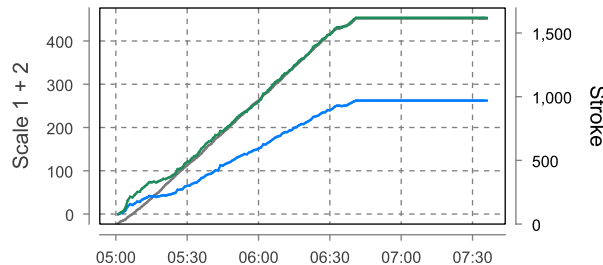
Belt scale 2 262.2 [t]

Deviation (BS1/BS2) 173 [%]

Muck Volume

Theoretical 217.1 [m³]

Net Stroke 1615 [mm]



Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 265 [L]

Polymer P003 0 [L]

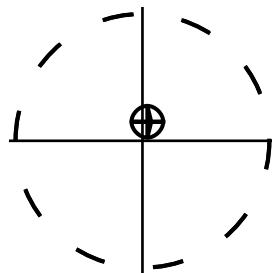
Water Foam Unit 13,305 [L]

HD Polymer 131 [L]

Bentonite (1+2) 55,481 [L]

4) TBM Guidance System

H	V
Deviation Front	
-2	5 [mm]
Deviation Center	
-5	7 [mm]
Deviation Rear	
-5	7 [mm]



Roll	-3 mm/m	-0.0 °
Nick	5 mm/m	-1.1 °

Note: Value before Ring Build

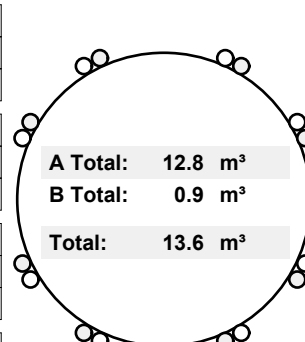
5) Grouting

#8	[m³]	[bar]
A	2.0	5.2
B	0.1	0.13

#7	[m³]	[bar]
A	2.0	5.1
B	0.1	1.41

#6	[m³]	[bar]
A	2.1	3.6
B	0.1	4.2

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0



A Total: 12.8 m³

B Total: 0.9 m³

Total: 13.6 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.2	5.1
B	0.2	5.8

#2	[m³]	[bar]
A	2.0	5.8
B	0.1	6.4

#3	[m³]	[bar]
A	2.1	5.2
B	0.1	5.0

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments
