

Install. Pos. (Leading Edge)

1677.578 m

Chainage Start

1669.664 m

Start Date

31/08/2024 07:36

Ring Type

U01

Chainage End

1667.973 m

Finish Date

31/08/2024 14:41

1) Operation Data

Advance Time

354 [min]

Ring Build Time

54 [min]


Downtime

17 [min]


2) Operation Data Diagrams

*Average Advance


	Avg*	Min	Max
CH Torque [MNm]	7.960		12.612




	Avg*	Min	Max
TBM Advance Rate [mm/min]	14		26




Thrust force [kN]	59569	19559	68779
-------------------	-------	-------	-------




Face support pressure crown [bar]	1.6	1.1	2.0
-----------------------------------	-----	-----	-----



Contact Force (Articulation)	15176	10074	17348
------------------------------	-------	-------	-------




Grout volume sum [m³]	14.6
-----------------------	------



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight	
Belt scale 1	583.1 [t]
Belt scale 2	314.6 [t]
Deviation (BS1/BS2)	185 [%]

Muck Volume	
Theoretical	227.9 [m³]
Net Stroke	1696 [mm]

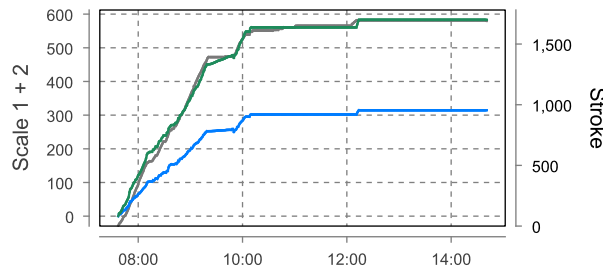


Ground Conditioning Volume	
Total Foam	100 [L]

Polymer P002	379 [L]
Polymer P003	0 [L]
Water Foam Unit	19,405 [L]
HD Polymer	251 [L]
Bentonite (1+2)	92,038 [L]

4) TBM Guidance System

H	V
Deviation Front	
-9	8 [mm]
Deviation Center	
-3	7 [mm]
Deviation Rear	
-3	7 [mm]

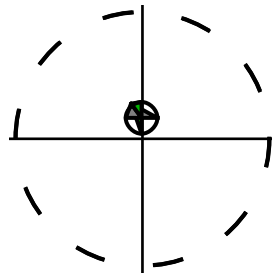

Roll	-3 mm/m	-0.0 °
Nick	5 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.2	4.4
B	0.1	0.01

#7	[m³]	[bar]
A	2.1	4.6
B	0.1	0.00

#6	[m³]	[bar]
A	2.4	3.2
B	0.2	3.8

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

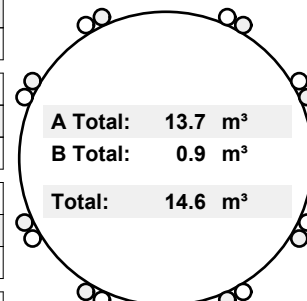

A Total: 13.7 m³

B Total: 0.9 m³

Total: 14.6 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.4	3.8
B	0.2	4.6

#2	[m³]	[bar]
A	2.1	4.3
B	0.1	4.3

#3	[m³]	[bar]
A	2.4	3.8
B	0.2	4.6

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

