

Install. Pos. (Leading Edge)

1675.974 m

Chainage Start

1667.973 m

Start Date

31/08/2024 14:41

Ring Type

U08

Chainage End

1666.463 m

Finish Date

31/08/2024 18:32

1) Operation Data

Advance Time

121 [min]

Ring Build Time

108 [min]

Downtime

0 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

8.922

13.599



TBM Advance Rate [mm/min]


Avg*

Min

Max

15

33




Thrust force [kN]

69413

19334

74184




Face support pressure crown [bar]

1.6

1.2

1.9




Contact Force (Articulation)

16742


10070

19842



Grout volume sum [m³]

12.3



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 452.4 [t]


Belt scale 2 333.5 [t]

Deviation (BS1/BS2) 136 [%]

Muck Volume

Theoretical 203.0 [m³]

Net Stroke 1510 [mm]

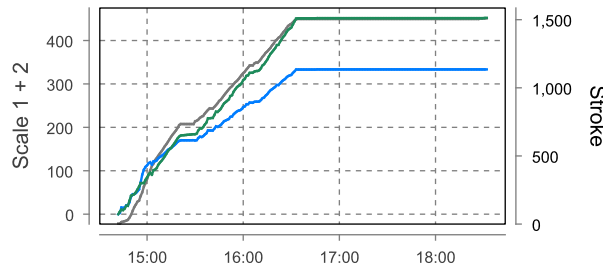

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 276 [L]

Polymer P003 0 [L]


Water Foam Unit 14,023 [L]

HD Polymer 462 [L]

Bentonite (1+2) 45,545 [L]

4) TBM Guidance System

H	V
Deviation Front	
-11	11 [mm]
Deviation Center	
-5	8 [mm]
Deviation Rear	
-5	8 [mm]

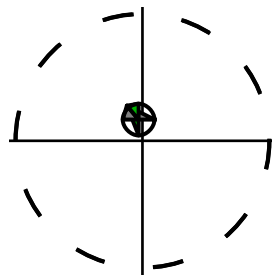

Roll	-2 mm/m	0.1 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	1.7	3.9
B	0.1	0.04

#7	[m³]	[bar]
A	1.6	4.2
B	0.1	0.03

#6	[m³]	[bar]
A	2.1	3.4
B	0.1	4.3

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

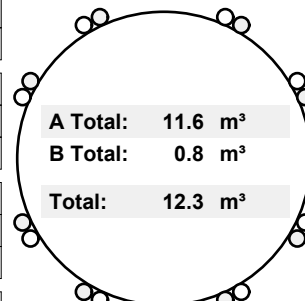

A Total: 11.6 m³

B Total: 0.8 m³

Total: 12.3 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	1.9	3.5
B	0.1	4.5

#2	[m³]	[bar]
A	1.8	3.9
B	0.1	4.8

#3	[m³]	[bar]
A	2.2	4.0
B	0.2	4.9

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

