

Install. Pos. (Leading Edge)

1674.372 m

Chainage Start

1666.463 m

Start Date

31/08/2024 18:32

Ring Type

U15

Chainage End

1664.875 m

Finish Date

01/09/2024 02:56

1) Operation Data

Advance Time

125 [min]

Ring Build Time

52 [min]

Downtime

328 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

8.714

17.223



TBM Advance Rate [mm/min]


Avg*

Min

Max

16

39




Thrust force [kN]

67358

20943

78495




Face support pressure crown [bar]

1.6

0.8

1.9




Contact Force (Articulation)

15861


8761

19913



Grout volume sum [m³]

14.8



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 477.2 [t]


Belt scale 2 247.4 [t]

Deviation (BS1/BS2) 193 [%]

Muck Volume

Theoretical 214.0 [m³]

Net Stroke 1593 [mm]

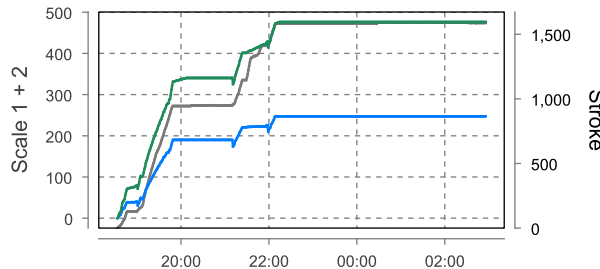

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 326 [L]

Polymer P003 0 [L]


Water Foam Unit 16,554 [L]

HD Polymer 629 [L]

Bentonite (1+2) 77,064 [L]

4) TBM Guidance System

H	V
Deviation Front	
-15	11 [mm]
Deviation Center	
-6	8 [mm]
Deviation Rear	
-6	8 [mm]

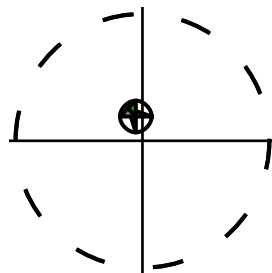

Roll	-3 mm/m	-0.0 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	1.9	3.8
B	0.1	1.06

#7	[m³]	[bar]
A	1.9	4.2
B	0.1	2.58

#6	[m³]	[bar]
A	2.3	3.3
B	0.2	4.0

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

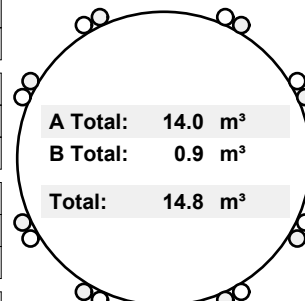

A Total: 14.0 m³

B Total: 0.9 m³

Total: 14.8 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.4	3.5
B	0.2	5.7

#2	[m³]	[bar]
A	1.8	3.5
B	0.1	4.3

#3	[m³]	[bar]
A	2.4	4.1
B	0.2	5.4

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

