

Install. Pos. (Leading Edge)

1672.771 m

Chainage Start

1664.875 m

Start Date

01/09/2024 02:56

Ring Type

U08

Chainage End

1663.266 m

Finish Date

01/09/2024 06:43

1) Operation Data

Advance Time

166 [min]

Ring Build Time

32 [min]

Downtime

30 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]


Avg*

Min

Max

9.977

17.518



TBM Advance Rate [mm/min]


Avg*

Min

Max

11

28




Thrust force [kN]

73939

23194

78623




Face support pressure crown [bar]

1.6

1.4

1.9




Contact Force (Articulation)

17304


9741

19825



Grout volume sum [m³]

15.1



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 524.9 [t]


Belt scale 2 257.4 [t]

Deviation (BS1/BS2) 204 [%]

Muck Volume

Theoretical 216.5 [m³]

Net Stroke 1612 [mm]

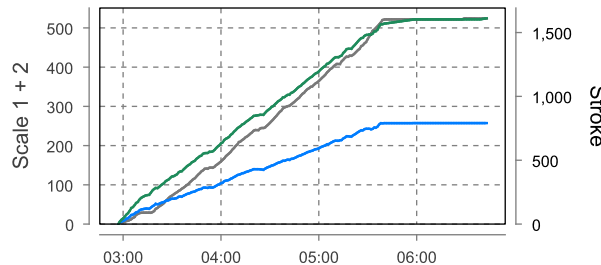

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 498 [L]

Polymer P003 0 [L]


Water Foam Unit 25,085 [L]

HD Polymer 212 [L]

Bentonite (1+2) 62,965 [L]

4) TBM Guidance System

H	V
Deviation Front	
-22	9 [mm]
Deviation Center	
-9	8 [mm]
Deviation Rear	
-9	8 [mm]

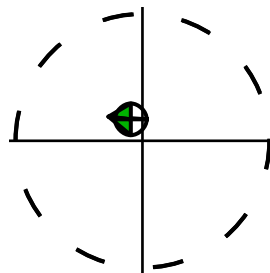

Roll	-1 mm/m	0.1 °
Nick	5 mm/m	-1.2 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.7	3.6
B	0.1	0.75

#7	[m³]	[bar]
A	1.4	3.3
B	0.1	3.11

#6	[m³]	[bar]
A	2.6	3.3
B	0.2	3.8

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

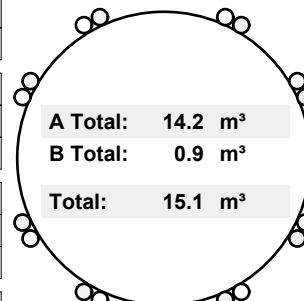

A Total: 14.2 m³

B Total: 0.9 m³

Total: 15.1 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	3.2	3.3
B	0.2	4.2

#2	[m³]	[bar]
A	2.1	3.3
B	0.1	4.0

#3	[m³]	[bar]
A	1.9	2.9
B	0.1	5.0

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

