

Install. Pos. (Leading Edge)

1667.971 m

Chainage Start

1660.072 m

Start Date

01/09/2024 22:30

Ring Type

U09

Chainage End

1658.465 m

Finish Date

02/09/2024 03:22

1) Operation Data

Advance Time

124 [min]

Ring Build Time

28 [min]

Downtime

136 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]


Avg*

Min

Max

11.223

17.467



TBM Advance Rate [mm/min]


Avg*

Min

Max

15

44




Thrust force [kN]

71168

18948

78302




Face support pressure crown [bar]

1.8

1.5

2.0




Contact Force (Articulation)

17443


9660

19421



Grout volume sum [m³]

14.2



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 465.4 [t]


Belt scale 2 234.1 [t]

Deviation (BS1/BS2) 199 [%]

Muck Volume

Theoretical 216.4 [m³]

Net Stroke 1611 [mm]

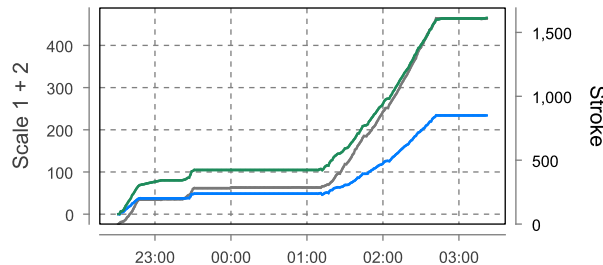

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 345 [L]

Polymer P003 0 [L]


Water Foam Unit 19,260 [L]

HD Polymer 253 [L]

Bentonite (1+2) 65,755 [L]

4) TBM Guidance System

H	V
Deviation Front	
-27	-13 [mm]
Deviation Center	
-9	0 [mm]
Deviation Rear	
-9	0 [mm]

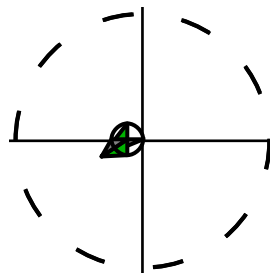

Roll	-4 mm/m	-0.1 °
Nick	3 mm/m	-1.3 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.6	3.7
B	0.1	0.40

#7	[m³]	[bar]
A	1.7	4.2
B	0.1	2.44

#6	[m³]	[bar]
A	2.4	3.0
B	0.1	4.0

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

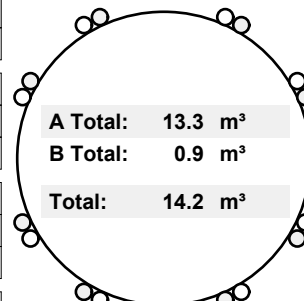

A Total: 13.3 m³

B Total: 0.9 m³

Total: 14.2 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.5	3.4
B	0.2	4.4

#2	[m³]	[bar]
A	1.9	3.7
B	0.1	4.8

#3	[m³]	[bar]
A	2.0	4.2
B	0.1	6.0

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

