

Install. Pos. (Leading Edge)

1666.366 m

Chainage Start

1658.465 m

Start Date

02/09/2024 03:22

Ring Type

U16

Chainage End

1656.842 m

Finish Date

02/09/2024 09:50

1) Operation Data

Advance Time

123 [min]

Ring Build Time

66 [min]


Downtime

196 [min]


2) Operation Data Diagrams

*Average Advance


	Avg*	Min	Max
CH Torque [MNm]	12.625		18.436




	Avg*	Min	Max
TBM Advance Rate [mm/min]	15		26




Thrust force [kN]	61269	16632	66238
-------------------	-------	-------	-------




Face support pressure crown [bar]	1.8	1.5	2.2
-----------------------------------	-----	-----	-----



Contact Force (Articulation)	19898	10209	22156
------------------------------	-------	-------	-------



Grout volume sum [m³]	13.5
-----------------------	------




3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1	605.0 [t]
Belt scale 2	400.7 [t]
Deviation (BS1/BS2)	151 [%]

Muck Volume

Theoretical	218.4 [m³]
Net Stroke	1625 [mm]

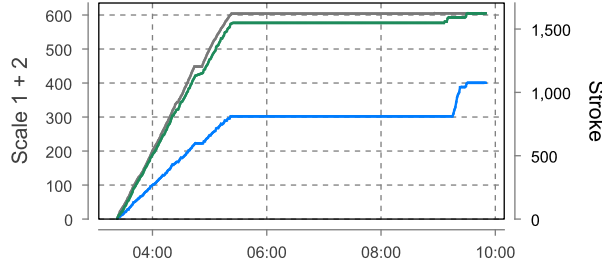


Ground Conditioning Volume

Total Foam	100 [L]
Polymer P002	300 [L]
Polymer P003	0 [L]
Water Foam Unit	15,067 [L]
HD Polymer	648 [L]
Bentonite (1+2)	66,167 [L]

4) TBM Guidance System

H	V
Deviation Front	
-29	-12 [mm]
Deviation Center	
-17	-2 [mm]
Deviation Rear	
-17	-2 [mm]

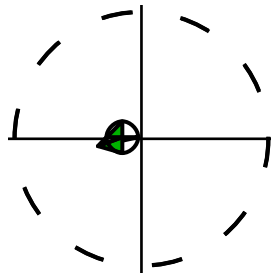

Roll	-8 mm/m	-0.3 °
Nick	4 mm/m	-1.2 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.1	3.9
B	0.1	0.03

#7	[m³]	[bar]
A	1.4	4.3
B	0.1	0.02

#6	[m³]	[bar]
A	2.4	3.6
B	0.2	4.4

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

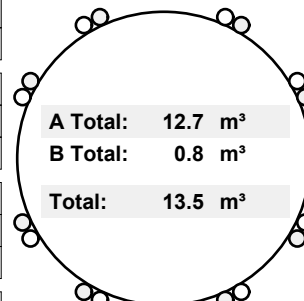

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.5	4.3
B	0.2	5.4

#2	[m³]	[bar]
A	2.0	4.4
B	0.1	5.1

#3	[m³]	[bar]
A	1.7	3.5
B	0.1	6.3

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

