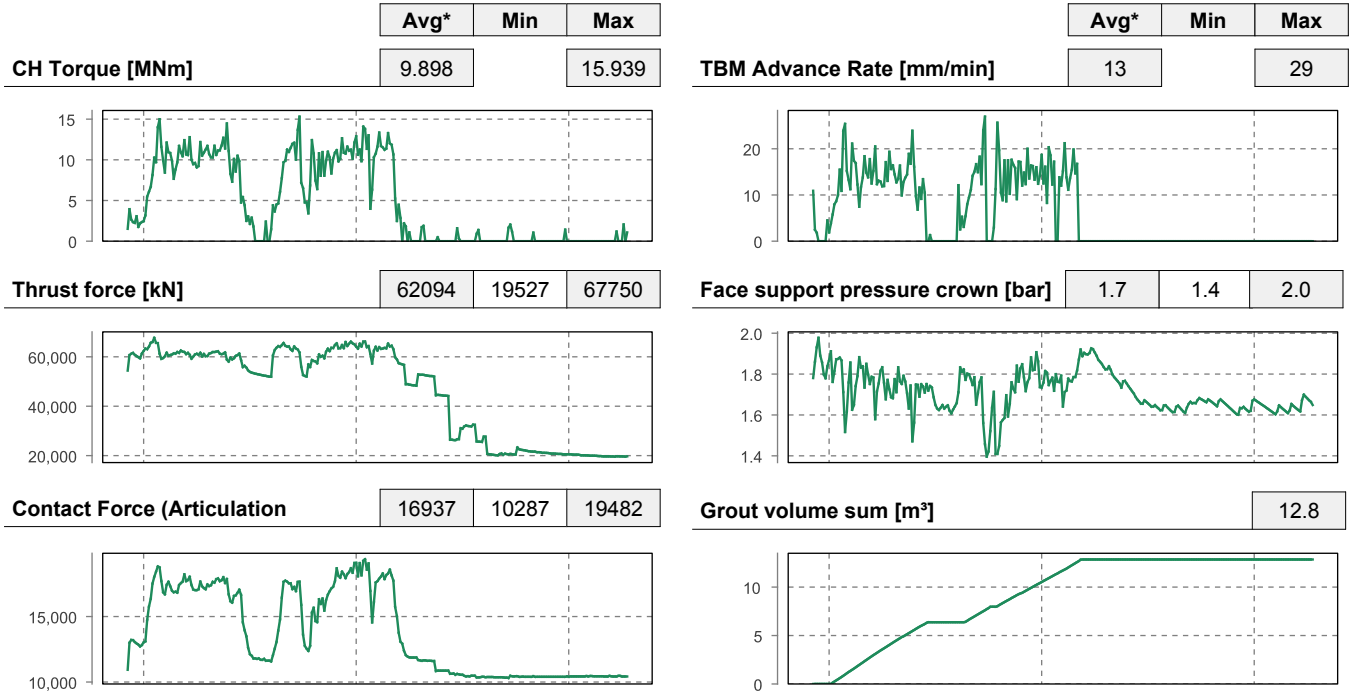
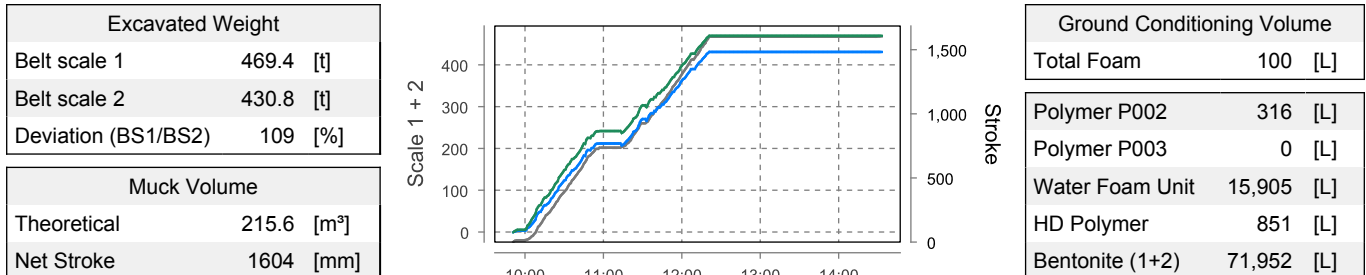



Install. Pos. (Leading Edge)	1664.764 m	Chainage Start	1656.842 m	Start Date	02/09/2024 09:50
Ring Type	U03	Chainage End	1655.238 m	Finish Date	02/09/2024 14:33

1) Operation Data

Advance Time	140 [min]	Ring Build Time	70 [min]	Downtime	78 [min]
--------------	-----------	-----------------	----------	----------	----------

2) Operation Data Diagrams
**Average Advance*

3) Muck Weight / Volume and Ground Conditioning

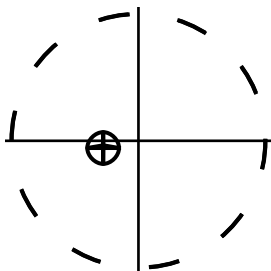4) TBM Guidance System

H	V
Deviation Front	
-30	-6 [mm]
Deviation Center	
-19	-5 [mm]
Deviation Rear	
-19	-5 [mm]



Roll	-8 mm/m	-0.3 °
Nick	5 mm/m	-1.2 °

Note: Value before Ring Build

5) Grouting

#8	[m³]	[bar]
A	1.8	4.0
B	0.1	0.17

#7	[m³]	[bar]
A	1.6	4.4
B	0.1	0.01

#6	[m³]	[bar]
A	2.6	3.8
B	0.2	5.2

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

#1	[m³]	[bar]
A	1.8	3.6
B	0.1	4.4

#2	[m³]	[bar]
A	1.8	3.8
B	0.1	4.9

#3	[m³]	[bar]
A	2.2	4.2
B	0.2	5.5

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

A Total: 12.0 m³
 B Total: 0.8 m³
 Total: 12.8 m³

Max. Volume [m³]
 avg. Pressure [bar]

6) Segments
