

Install. Pos. (Leading Edge)

1663.163 m

Chainage Start

1655.238 m

Start Date

02/09/2024 14:33

Ring Type

U08

Chainage End

1653.642 m

Finish Date

02/09/2024 17:20

1) Operation Data

Advance Time

121 [min]

Ring Build Time

41 [min]


Downtime

0 [min]


2) Operation Data Diagrams

*Average Advance


	Avg*	Min	Max
CH Torque [NMm]	11.070		17.023




	Avg*	Min	Max
TBM Advance Rate [mm/min]	14		27




Thrust force [kN]	65742	20138	70967
-------------------	-------	-------	-------




Face support pressure crown [bar]	1.7	1.4	2.0
-----------------------------------	-----	-----	-----



Contact Force (Articulation)	17706	10362	20395
------------------------------	-------	-------	-------



Grout volume sum [m³]	13.1
-----------------------	------




3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1	431.0 [t]
Belt scale 2	411.8 [t]
Deviation (BS1/BS2)	105 [%]

Muck Volume

Theoretical	214.4 [m³]
Net Stroke	1596 [mm]

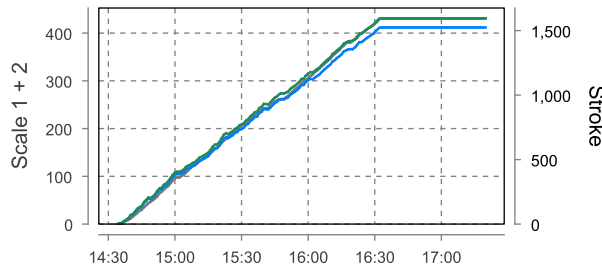


Ground Conditioning Volume

Total Foam	100 [L]
------------	---------

Polymer P002	298 [L]
Polymer P003	0 [L]
Water Foam Unit	15,003 [L]
HD Polymer	634 [L]
Bentonite (1+2)	57,455 [L]

4) TBM Guidance System

H	V
Deviation Front	
-25	-5 [mm]
Deviation Center	
-21	-6 [mm]
Deviation Rear	
-21	-6 [mm]

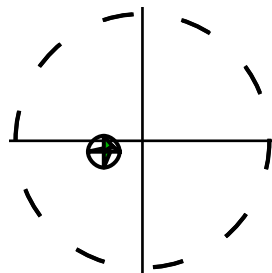

Roll	-3 mm/m	-0.0 °
Nick	5 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.1	4.8
B	0.1	0.16

#7	[m³]	[bar]
A	1.8	5.8
B	0.1	0.03

#6	[m³]	[bar]
A	2.5	4.3
B	0.2	5.6

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

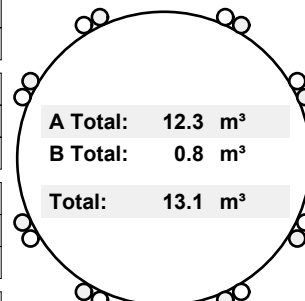

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	1.9	4.3
B	0.1	5.2

#2	[m³]	[bar]
A	1.9	4.4
B	0.1	4.9

#3	[m³]	[bar]
A	2.1	4.7
B	0.1	6.0

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

