

Install. Pos. (Leading Edge)

1661.561 m

Chainage Start

1653.642 m

Start Date

02/09/2024 17:20

Ring Type

U01

Chainage End

1652.035 m

Finish Date

02/09/2024 20:25

1) Operation Data

Advance Time

114 [min]

Ring Build Time

55 [min]

Downtime

16 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

11.232

19.220



TBM Advance Rate [mm/min]


Avg*

Min

Max

15

35




Thrust force [kN]

63600

18047

67750




Face support pressure crown [bar]

1.8

1.3

2.0




Contact Force (Articulation)

17752


10250

20018



Grout volume sum [m³]

11.2



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 409.8 [t]


Belt scale 2 385.5 [t]

Deviation (BS1/BS2) 106 [%]

Muck Volume

Theoretical 216.0 [m³]

Net Stroke 1608 [mm]

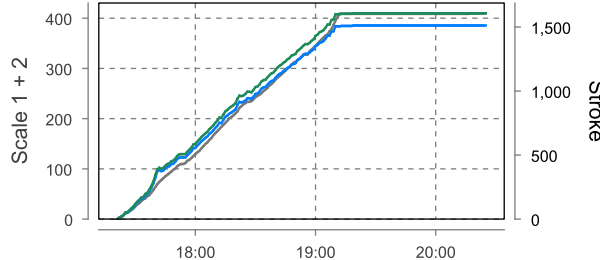

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 286 [L]

Polymer P003 0 [L]


Water Foam Unit 14,403 [L]

HD Polymer 379 [L]

Bentonite (1+2) 51,537 [L]

4) TBM Guidance System

H	V
Deviation Front	
-17	-4 [mm]
Deviation Center	
-20	-6 [mm]
Deviation Rear	
-20	-6 [mm]

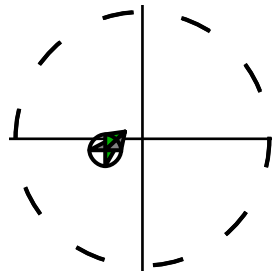

Roll	-2 mm/m	0.0 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build

5) Grouting

#8	[m³]	[bar]
A	1.7	4.6
B	0.1	1.71

#7	[m³]	[bar]
A	1.5	5.1
B	0.1	1.59

#6	[m³]	[bar]
A	2.5	3.7
B	0.2	4.7


#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

#1	[m³]	[bar]
A	1.1	2.6
B	0.1	2.9

#2	[m³]	[bar]
A	2.0	4.0
B	0.1	4.7

#3	[m³]	[bar]
A	1.6	4.8
B	0.1	5.0

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

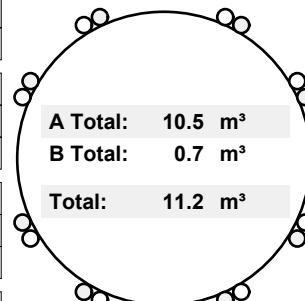

A Total: 10.5 m³

B Total: 0.7 m³

Total: 11.2 m³

Max. Volume [m³]

avg. Pressure [bar]

6) Segments

