


Install. Pos. (Leading Edge)	1659.958 m	Chainage Start	1652.035 m	Start Date	02/09/2024 20:25
Ring Type	U14	Chainage End	1650.459 m	Finish Date	03/09/2024 00:11

1) Operation Data

Advance Time	159 [min]	Ring Build Time	53 [min]	Downtime	13 [min]
--------------	-----------	-----------------	----------	----------	----------


2) Operation Data Diagrams

*Average Advance

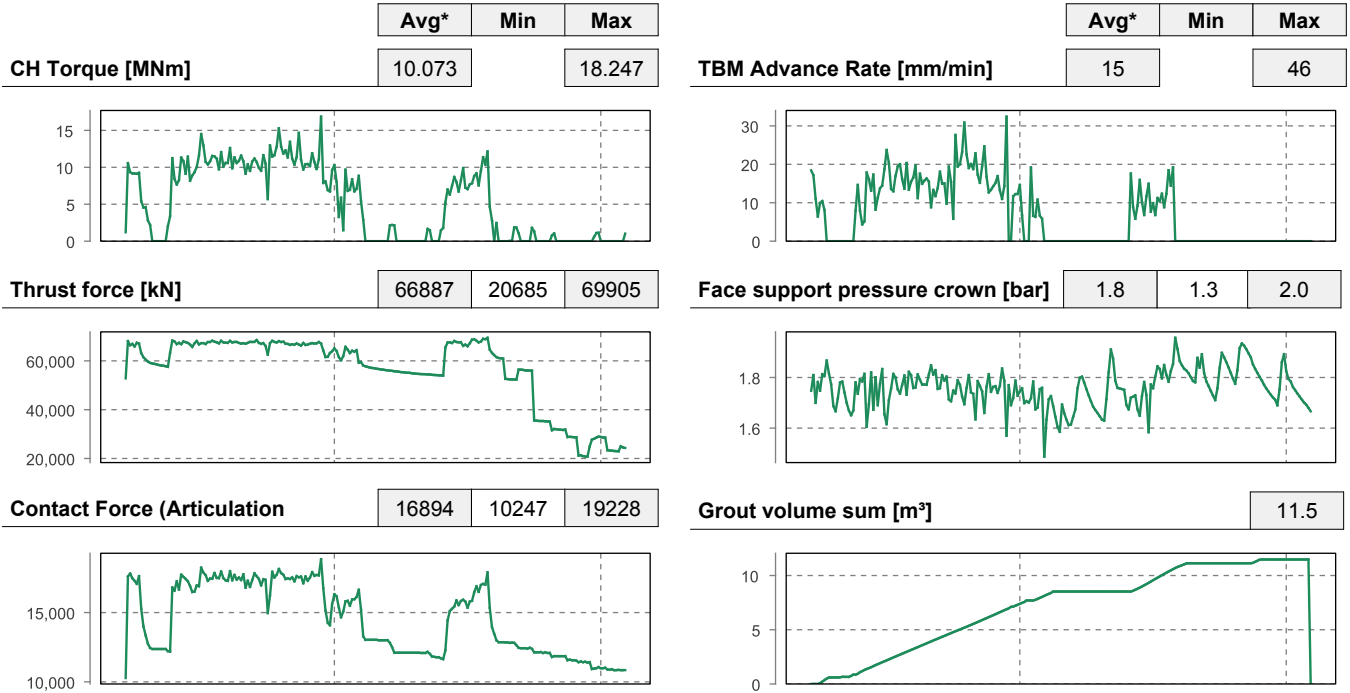

3) Muck Weight / Volume and Ground Conditioning


Excavated Weight	
Belt scale 1	413.5 [t]
Belt scale 2	382.7 [t]
Deviation (BS1/BS2)	108 [%]
Muck Volume	
Theoretical	212.3 [m³]
Net Stroke	1580 [mm]

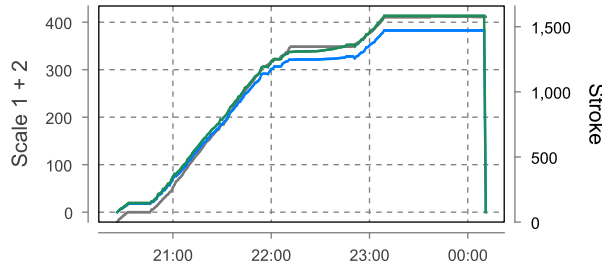

Ground Conditioning Volume	
Total Foam	100 [L]
Polymer P002	300 [L]
Polymer P003	0 [L]
Water Foam Unit	15,144 [L]
HD Polymer	488 [L]
Bentonite (1+2)	65,569 [L]

4) TBM Guidance System

H	V
Deviation Front	
-10	0 [mm]
Deviation Center	
-19	-7 [mm]
Deviation Rear	
-19	-7 [mm]

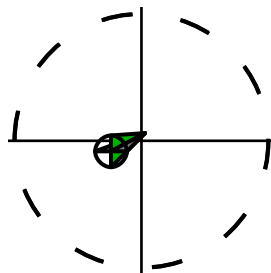

Roll	-3 mm/m	-0.1 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	1.2	3.6
B	0.1	0.17

#7	[m³]	[bar]
A	1.3	3.8
B	0.1	1.94

#6	[m³]	[bar]
A	2.7	3.5
B	0.2	5.1

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

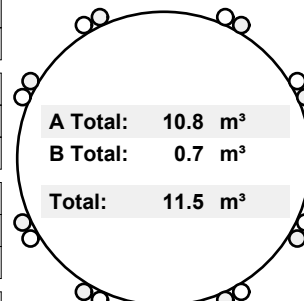

Max. Volume [m³]	
avg. Pressure [bar]	

#1	[m³]	[bar]
A	1.4	3.7
B	0.1	4.8

#2	[m³]	[bar]
A	1.9	3.9
B	0.1	4.6

#3	[m³]	[bar]
A	1.4	4.9
B	0.1	4.7

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

