

Install. Pos. (Leading Edge)

1658.358 m

Chainage Start

1650.459 m

Start Date

03/09/2024 00:11

Ring Type

U05

Chainage End

1648.853 m

Finish Date

03/09/2024 05:10

1) Operation Data

Advance Time

125 [min]

Ring Build Time

79 [min]

Downtime

96 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]


Avg*

Min

Max

10.723

16.764



TBM Advance Rate [mm/min]


Avg*

Min

Max

15

37




Thrust force [kN]

71891

21940

76886




Face support pressure crown [bar]

1.7

1.5

2.0




Contact Force (Articulation)

17488


10739

20249



Grout volume sum [m³]

11.8



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 416.1 [t]


Belt scale 2 378.4 [t]

Deviation (BS1/BS2) 110 [%]

Muck Volume

Theoretical 216.5 [m³]

Net Stroke 1611 [mm]

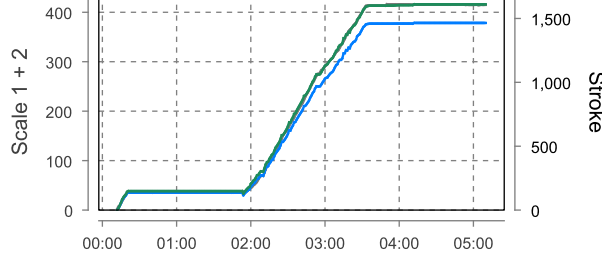

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 312 [L]

Polymer P003 0 [L]


Water Foam Unit 15,757 [L]

HD Polymer 454 [L]

Bentonite (1+2) 58,720 [L]

4) TBM Guidance System

H	V
Deviation Front	
-7	-1 [mm]
Deviation Center	
-16	-8 [mm]
Deviation Rear	
-16	-8 [mm]

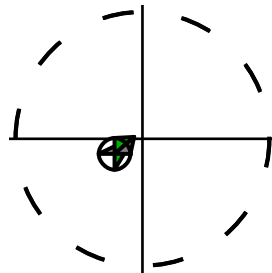

Roll	-0 mm/m	0.1 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	1.4	4.6
B	0.1	0.16

#7	[m³]	[bar]
A	1.6	4.7
B	0.1	1.21

#6	[m³]	[bar]
A	2.5	4.4
B	0.2	5.9

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

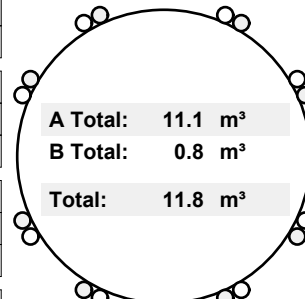

Max. Volume [m³]
avg. Pressure [bar]

#1	[m³]	[bar]
A	2.0	4.6
B	0.1	5.5

#2	[m³]	[bar]
A	1.8	4.3
B	0.1	5.1

#3	[m³]	[bar]
A	1.4	5.2
B	0.1	5.3

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

