

Install. Pos. (Leading Edge)

1653.552 m

Chainage Start

1645.644 m

Start Date

05/09/2024 12:32

Ring Type

U02

Chainage End

1644.051 m

Finish Date

05/09/2024 15:19

1) Operation Data

Advance Time

96 [min]

Ring Build Time

52 [min]

Downtime

17 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

8.983

16.850


TBM Advance Rate [mm/min]


Avg*

Min

Max

18


55


Thrust force [kN]

62539

22262


77948


Face support pressure crown [bar]

1.7

1.4


1.9


Contact Force (Articulation)


16206

10515

20090


Grout volume sum [m³]

11.9


3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 434.4 [t]

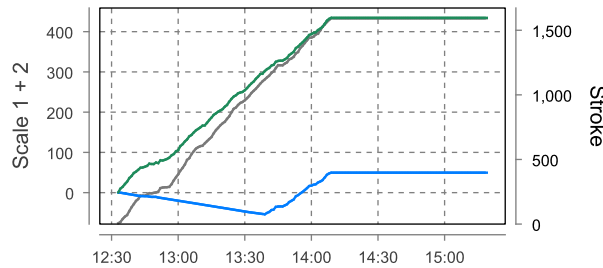
Belt scale 2 49.7 [t]

Deviation (BS1/BS2) 875 [%]

Muck Volume

Theoretical 214.0 [m³]

Net Stroke 1593 [mm]



Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 269 [L]

Polymer P003 0 [L]

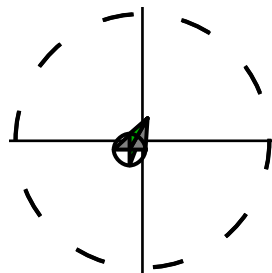
Water Foam Unit 13,577 [L]

HD Polymer 154 [L]

Bentonite (1+2) 45,648 [L]

4) TBM Guidance System

H	V
Deviation Front	
-10	-8 [mm]
Deviation Center	
-12	-9 [mm]
Deviation Rear	
-12	-9 [mm]



Roll	-4 mm/m	-0.1 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build

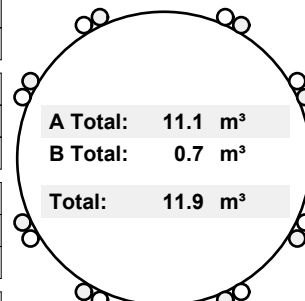
5) Grouting

#8	[m³]	[bar]
A	2.3	4.0
B	0.1	0.29

#7	[m³]	[bar]
A	1.7	6.4
B	0.1	3.34

#6	[m³]	[bar]
A	2.0	3.8
B	0.1	4.9

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0


A Total: 11.1 m³
B Total: 0.7 m³
Total: 11.9 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.3	7.0
B	0.1	12.3

#2	[m³]	[bar]
A	0.4	5.3
B	0.0	2.5

#3	[m³]	[bar]
A	2.2	4.6
B	0.1	6.3

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments
