

Install. Pos. (Leading Edge)

1651.948 m

Chainage Start

1644.051 m

Start Date

05/09/2024 15:19

Ring Type

U09

Chainage End

1642.447 m

Finish Date

05/09/2024 20:22

1) Operation Data

Advance Time

110 [min]

Ring Build Time

53 [min]


Downtime

137 [min]


2) Operation Data Diagrams

*Average Advance


	Avg*	Min	Max
CH Torque [MNm]	9.911		15.417




	Avg*	Min	Max
TBM Advance Rate [mm/min]	15		33




Thrust force [kN]	56987	17661	62635
-------------------	-------	-------	-------




Face support pressure crown [bar]	1.6	1.4	1.8
-----------------------------------	-----	-----	-----



Contact Force (Articulation)	16427	9541	19180
------------------------------	-------	------	-------




Grout volume sum [m³]	13.6
-----------------------	------



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight	
Belt scale 1	460.8 [t]
Belt scale 2	371.6 [t]
Deviation (BS1/BS2)	124 [%]

Muck Volume	
Theoretical	215.7 [m³]
Net Stroke	1605 [mm]

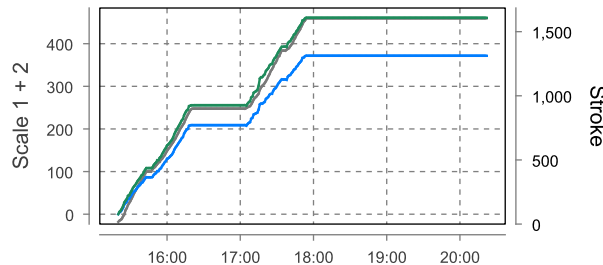


Ground Conditioning Volume	
Total Foam	100 [L]

Polymer P002	419 [L]
Polymer P003	0 [L]
Water Foam Unit	21,082 [L]
HD Polymer	181 [L]
Bentonite (1+2)	19,531 [L]

4) TBM Guidance System

H	V
Deviation Front	
-8	-1 [mm]
Deviation Center	
-10	-6 [mm]
Deviation Rear	
-10	-6 [mm]

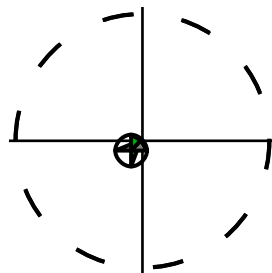

Roll	-2 mm/m	0.0 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.7	4.6
B	0.1	0.25

#7	[m³]	[bar]
A	2.0	6.3
B	0.1	2.43

#6	[m³]	[bar]
A	2.3	3.8
B	0.2	4.6

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

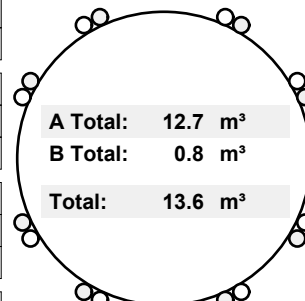

A Total: 12.7 m³

B Total: 0.8 m³

Total: 13.6 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	3.2	7.3
B	0.2	14.3

#2	[m³]	[bar]
A	0.1	10.1
B	0.0	0.7

#3	[m³]	[bar]
A	2.3	4.9
B	0.2	5.8

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

