

Install. Pos. (Leading Edge)

1650.348 m

Chainage Start

1642.447 m

Start Date

05/09/2024 20:22

Ring Type

U16

Chainage End

1640.824 m

Finish Date

05/09/2024 22:55

1) Operation Data

Advance Time

113 [min]

Ring Build Time

33 [min]

Downtime

0 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

8.552

15.256



TBM Advance Rate [mm/min]


Avg*

Min

Max

17

36




Thrust force [kN]

61062

19366

70677




Face support pressure crown [bar]

1.6

1.5

1.9




Contact Force (Articulation)

15850


9100

19747



Grout volume sum [m³]

13.4



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 493.5 [t]


Belt scale 2 381.9 [t]

Deviation (BS1/BS2) 129 [%]

Muck Volume

Theoretical 218.0 [m³]

Net Stroke 1623 [mm]

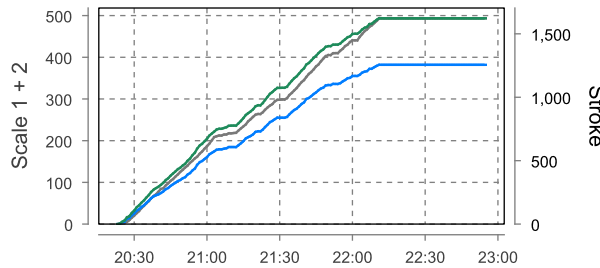

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 368 [L]

Polymer P003 0 [L]


Water Foam Unit 18,678 [L]

HD Polymer 204 [L]

Bentonite (1+2) 33,306 [L]

4) TBM Guidance System

H	V
Deviation Front	
-10	-3 [mm]
Deviation Center	
-6	-7 [mm]
Deviation Rear	
-6	-7 [mm]

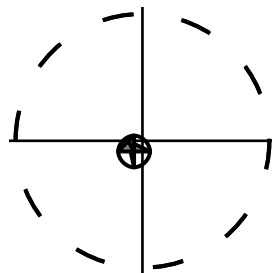

Roll	-3 mm/m	-0.0 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	1.8	3.8
B	0.1	1.51

#7	[m³]	[bar]
A	1.4	4.6
B	0.1	2.36

#6	[m³]	[bar]
A	2.3	3.9
B	0.2	5.1

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

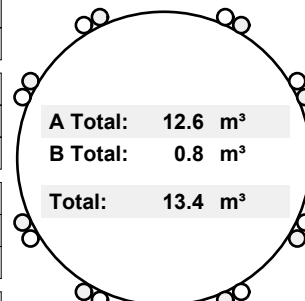

#1	[m³]	[bar]
A	1.2	3.6
B	0.1	7.3

#2	[m³]	[bar]
A	3.5	2.5
B	0.2	4.1

#3	[m³]	[bar]
A	2.3	4.6
B	0.2	6.1

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

Max. Volume [m³]

avg. Pressure [bar]

6) Segments

