

Install. Pos. (Leading Edge)

1648.748 m

Chainage Start

1640.824 m

Start Date

05/09/2024 22:55

Ring Type

U11

Chainage End

1639.224 m

Finish Date

06/09/2024 01:38

1) Operation Data

Advance Time

87 [min]

Ring Build Time

50 [min]

Downtime

28 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

9.297

15.097



TBM Advance Rate [mm/min]


Avg*

Min

Max

20

38




Thrust force [kN]

59091

22680

64726




Face support pressure crown [bar]

1.6

1.4

1.8




Contact Force (Articulation)

15597


9361

18393



Grout volume sum [m³]

12.5



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 390.3 [t]


Belt scale 2 295.7 [t]

Deviation (BS1/BS2) 132 [%]

Muck Volume

Theoretical 215.1 [m³]

Net Stroke 1601 [mm]

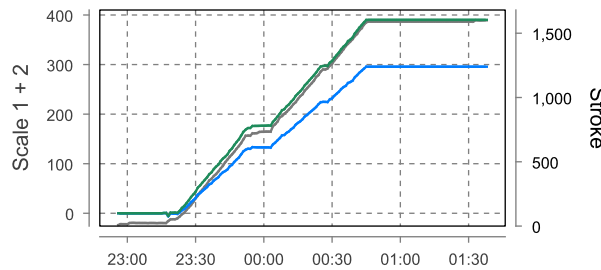

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 338 [L]

Polymer P003 0 [L]


Water Foam Unit 17,280 [L]

HD Polymer 212 [L]

Bentonite (1+2) 30,492 [L]

4) TBM Guidance System

H	V
Deviation Front	
-13	-4 [mm]
Deviation Center	
-7	-8 [mm]
Deviation Rear	
-7	-8 [mm]

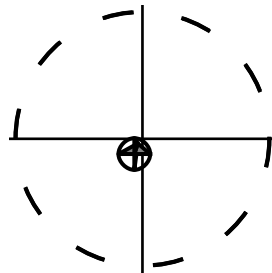

Roll	-3 mm/m	-0.0 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	1.7	4.0
B	0.1	0.60

#7	[m³]	[bar]
A	1.2	4.8
B	0.1	2.70

#6	[m³]	[bar]
A	2.0	4.0
B	0.1	5.8

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

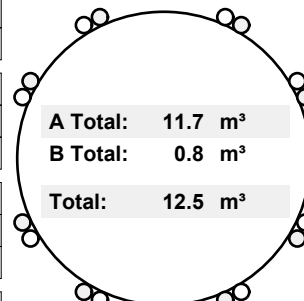

A Total: 11.7 m³

B Total: 0.8 m³

Total: 12.5 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	1.2	4.8
B	0.1	9.7

#2	[m³]	[bar]
A	3.7	3.0
B	0.3	5.9

#3	[m³]	[bar]
A	1.7	4.7
B	0.1	6.3

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

