

Install. Pos. (Leading Edge)

1647.148 m

Chainage Start

1639.224 m

Start Date

06/09/2024 01:38

Ring Type

U04

Chainage End

1637.598 m

Finish Date

06/09/2024 06:13

1) Operation Data

Advance Time

115 [min]

Ring Build Time

43 [min]


Downtime

119 [min]


2) Operation Data Diagrams

*Average Advance


	Avg*	Min	Max
CH Torque [MNm]	9.470		15.319




	Avg*	Min	Max
TBM Advance Rate [mm/min]	18		37




	Avg*	Min	Max
Thrust force [kN]	59812	20331	68554




	Avg*	Min	Max
Face support pressure crown [bar]	1.6	1.4	1.8



	Avg*	Min	Max
Contact Force (Articulation)	15660	9765	18753




	Avg*	Min	Max
Grout volume sum [m³]	13.0		



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight	
Belt scale 1	416.8 [t]
Belt scale 2	299.2 [t]
Deviation (BS1/BS2)	139 [%]

Muck Volume	
Theoretical	218.6 [m³]
Net Stroke	1627 [mm]

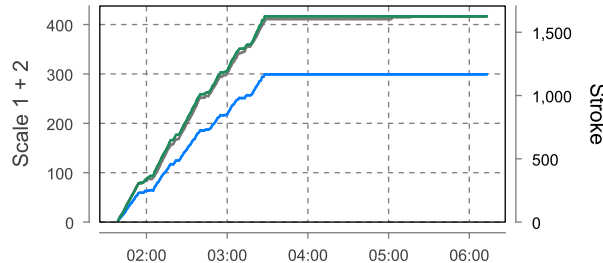


Ground Conditioning Volume	
Total Foam	100 [L]

Polymer P002	442 [L]
Polymer P003	0 [L]
Water Foam Unit	23,862 [L]
HD Polymer	264 [L]
Bentonite (1+2)	36,423 [L]

4) TBM Guidance System

H	V
Deviation Front	
-16	-7 [mm]
Deviation Center	
-8	-10 [mm]
Deviation Rear	
-8	-10 [mm]

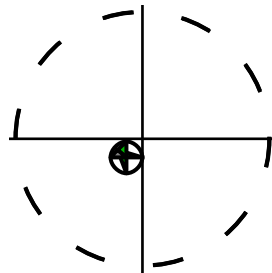

Roll	-0 mm/m	0.1 °
Nick	6 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.7	4.3
B	0.1	0.30

#7	[m³]	[bar]
A	1.8	5.1
B	0.1	2.34

#6	[m³]	[bar]
A	2.1	3.1
B	0.2	4.5

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

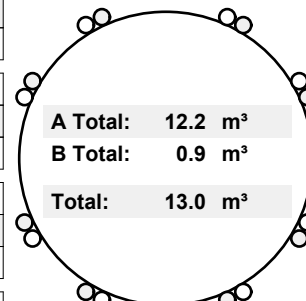

A Total: 12.2 m³
B Total: 0.9 m³
Total: 13.0 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	1.5	4.3
B	0.1	10.2

#2	[m³]	[bar]
A	2.1	2.0
B	0.1	3.3

#3	[m³]	[bar]
A	2.1	3.9
B	0.1	6.2

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

