

Install. Pos. (Leading Edge)

1645.545 m

Chainage Start

1637.598 m

Start Date

06/09/2024 06:13

Ring Type

U11

Chainage End

1636.005 m

Finish Date

06/09/2024 10:43

1) Operation Data

Advance Time

124 [min]

Ring Build Time

30 [min]

Downtime

108 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [NMm]


Avg*

Min

Max

5.753

12.566



TBM Advance Rate [mm/min]


Avg*

Min

Max

14

35




Thrust force [kN]

67700

23130

74666




Face support pressure crown [bar]

1.6

1.4

1.8




Contact Force (Articulation)

14404


10728

17294



Grout volume sum [m³]

13.1



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 455.9 [t]


Belt scale 2 306.6 [t]

Deviation (BS1/BS2) 149 [%]

Muck Volume

Theoretical 214.1 [m³]

Net Stroke 1593 [mm]

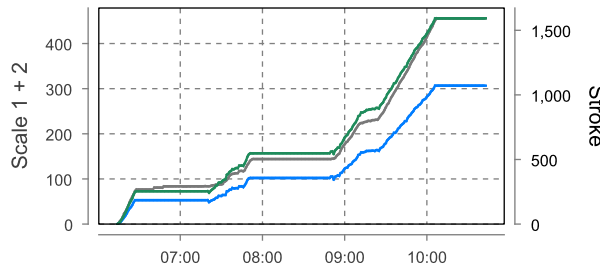

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 472 [L]

Polymer P003 0 [L]


Water Foam Unit 24,021 [L]

HD Polymer 344 [L]

Bentonite (1+2) 48,330 [L]

4) TBM Guidance System

H	V
Deviation Front	
-16	-10 [mm]
Deviation Center	
-7	-11 [mm]
Deviation Rear	
-7	-11 [mm]

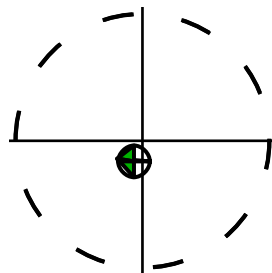

Roll	-1 mm/m	0.0 °
Nick	5 mm/m	-1.1 °

Note: Value before Ring Build


5) Grouting

#8	[m³]	[bar]
A	2.2	3.4
B	0.1	0.29

#7	[m³]	[bar]
A	1.8	4.8
B	0.1	2.54

#6	[m³]	[bar]
A	2.0	2.6
B	0.1	3.2

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

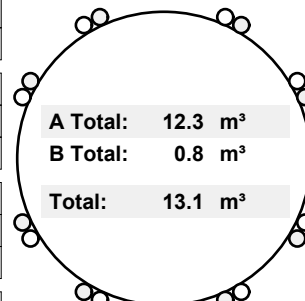

A Total: 12.3 m³

B Total: 0.8 m³

Total: 13.1 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.2	4.2
B	0.2	5.4

#2	[m³]	[bar]
A	2.1	2.3
B	0.1	3.2

#3	[m³]	[bar]
A	2.0	3.5
B	0.1	5.5

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments

