

Install. Pos. (Leading Edge)

1642.337 m

Chainage Start

1634.436 m

Start Date

06/09/2024 13:42

Ring Type

U04

Chainage End

1632.830 m

Finish Date

06/09/2024 16:05

1) Operation Data

Advance Time

198 [min]

Ring Build Time

26 [min]

Downtime

0 [min]


2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]
Avg*
Min
Max


9.070

14.970


TBM Advance Rate [mm/min]
Avg*
Min
Max

15


43


Thrust force [kN]

67000

23613


72061


Face support pressure crown [bar]

1.8

1.5


1.9


Contact Force (Articulation)


15918

9636

17372


Grout volume sum [m³]

14.9


3) Muck Weight / Volume and Ground Conditioning
Excavated Weight

Belt scale 1 441.1 [t]

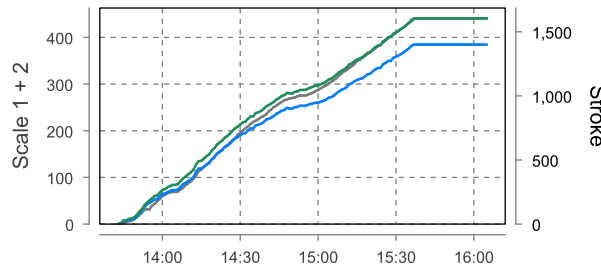
Belt scale 2 384.6 [t]

Deviation (BS1/BS2) 115 [%]

Muck Volume

Theoretical 216.5 [m³]

Net Stroke 1611 [mm]


Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 333 [L]

Polymer P003 0 [L]

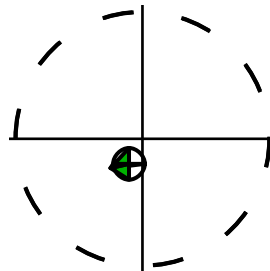
Water Foam Unit 16,054 [L]

HD Polymer 146 [L]

Bentonite (1+2) 40,867 [L]

4) TBM Guidance System

H	V
Deviation Front	
-20	-16 [mm]
Deviation Center	
-8	-14 [mm]
Deviation Rear	
-8	-14 [mm]



Roll	-4 mm/m	-0.1 °
Nick	5 mm/m	-1.1 °

Note: Value before Ring Build

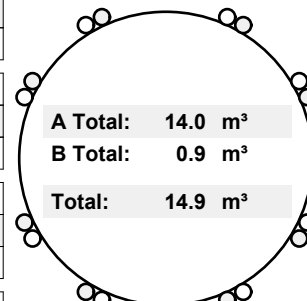
5) Grouting

#8	[m³]	[bar]
A	2.5	4.5
B	0.1	0.35

#7	[m³]	[bar]
A	1.5	4.6
B	0.1	3.50

#6	[m³]	[bar]
A	2.3	3.5
B	0.2	4.1

#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0


A Total: 14.0 m³
B Total: 0.9 m³
Total: 14.9 m³

Max. Volume [m³]

avg. Pressure [bar]

#1	[m³]	[bar]
A	2.8	3.7
B	0.2	5.4

#2	[m³]	[bar]
A	2.8	2.9
B	0.2	3.9

#3	[m³]	[bar]
A	2.0	4.0
B	0.1	5.7

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

6) Segments
