

Install. Pos. (Leading Edge)

1639.138 m

Chainage Start

1631.216 m

Start Date

06/09/2024 19:58

Ring Type

U15

Chainage End

1629.611 m

Finish Date

06/09/2024 22:54

1) Operation Data

Advance Time

97 [min]

Ring Build Time

42 [min]

Downtime

36 [min]

2) Operation Data Diagrams

*Average Advance

CH Torque [MNm]


Avg*

Min

Max

10.821

15.251



TBM Advance Rate [mm/min]


Avg*

Min

Max

18

36




Thrust force [kN]

64727

20589

72704




Face support pressure crown [bar]

1.6

1.4

1.9




Contact Force (Articulation)

16833


9378

19438



Grout volume sum [m³]

13.7



3) Muck Weight / Volume and Ground Conditioning

Excavated Weight

Belt scale 1 449.1 [t]


Belt scale 2 391.4 [t]

Deviation (BS1/BS2) 115 [%]

Muck Volume

Theoretical 216.2 [m³]

Net Stroke 1609 [mm]

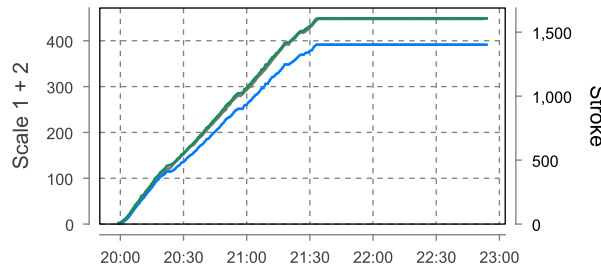

Ground Conditioning Volume

Total Foam 100 [L]

Polymer P002 318 [L]

Polymer P003 0 [L]


Water Foam Unit 15,282 [L]

HD Polymer 219 [L]

Bentonite (1+2) 38,775 [L]

4) TBM Guidance System

H	V
Deviation Front	
-26	-23 [mm]
Deviation Center	
-11	-17 [mm]
Deviation Rear	
-11	-17 [mm]

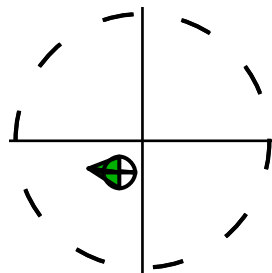

Roll	-4 mm/m	-0.1 °
Nick	4 mm/m	-1.2 °

Note: Value before Ring Build

5) Grouting

#8	[m³]	[bar]
A	1.8	3.9
B	0.1	1.97

#7	[m³]	[bar]
A	1.4	4.5
B	0.1	1.99

#6	[m³]	[bar]
A	2.0	3.7
B	0.1	4.6


#5	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

#1	[m³]	[bar]
A	2.2	3.7
B	0.2	5.0

#2	[m³]	[bar]
A	2.6	4.1
B	0.2	5.7

#3	[m³]	[bar]
A	2.0	4.3
B	0.1	5.8

#4	[m³]	[bar]
A	0.0	0.0
B	0.0	0.0

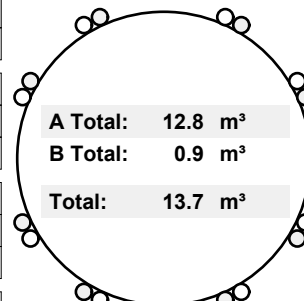

Max. Volume [m³]

avg. Pressure [bar]

6) Segments

