

Install. Pos. (Leading Edge)

1671.166 m

Chainage Start

1663.266 m

Start Date

01/09/2024 06:43

Ring Type

U01

Chainage End

1661.646 m

Finish Date

01/09/2024 18:23

**1) Operation Data**

Advance Time

131 [min]

Ring Build Time

75 [min]

Downtime

489 [min]

**2) Operation Data Diagrams**

\*Average Advance

**CH Torque [NMm]**


Avg\*

Min

Max

8.220

13.784


**TBM Advance Rate [mm/min]**


Avg\*

Min

Max

13


27


**Thrust force [kN]**

71338

16085


81197


**Face support pressure crown [bar]**

1.8

1.2


2.1


**Contact Force (Articulation)**


16236

9928

19279


**Grout volume sum [m³]**

14.7


**3) Muck Weight / Volume and Ground Conditioning**
**Excavated Weight**

Belt scale 1 634.9 [t]

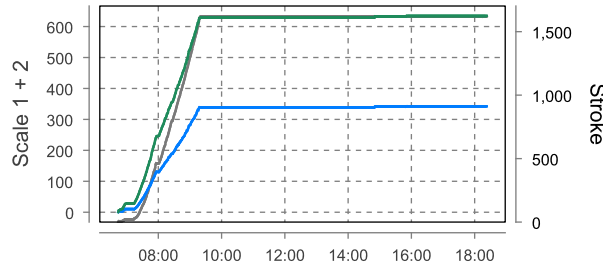
Belt scale 2 342.2 [t]

Deviation (BS1/BS2) 186 [%]

**Muck Volume**

Theoretical 217.8 [m³]

Net Stroke 1621 [mm]


**Ground Conditioning Volume**

Total Foam 100 [L]

Polymer P002 460 [L]

Polymer P003 0 [L]

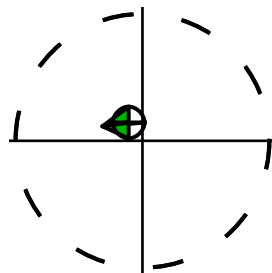
Water Foam Unit 23,196 [L]

HD Polymer 341 [L]

Bentonite (1+2) 83,044 [L]

**4) TBM Guidance System**

| H                | V      |
|------------------|--------|
| Deviation Front  |        |
| -29              | 3 [mm] |
| Deviation Center |        |
| -8               | 5 [mm] |
| Deviation Rear   |        |
| -8               | 5 [mm] |



|      |         |        |
|------|---------|--------|
| Roll | -3 mm/m | -0.1 ° |
| Nick | 5 mm/m  | -1.2 ° |

Note: Value before Ring Build

**5) Grouting**

| #8 | [m³] | [bar] |
|----|------|-------|
| A  | 2.0  | 2.9   |
| B  | 0.1  | 0.03  |

| #7 | [m³] | [bar] |
|----|------|-------|
| A  | 1.6  | 3.1   |
| B  | 0.1  | 0.02  |

| #6 | [m³] | [bar] |
|----|------|-------|
| A  | 2.8  | 3.0   |
| B  | 0.2  | 4.5   |

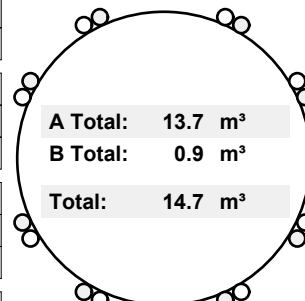
| #5 | [m³] | [bar] |
|----|------|-------|
| A  | 0.0  | 0.0   |
| B  | 0.0  | 0.0   |

| #1 | [m³] | [bar] |
|----|------|-------|
| A  | 2.5  | 2.6   |
| B  | 0.2  | 3.8   |

| #2 | [m³] | [bar] |
|----|------|-------|
| A  | 1.7  | 2.8   |
| B  | 0.1  | 3.5   |

| #3 | [m³] | [bar] |
|----|------|-------|
| A  | 2.4  | 3.5   |
| B  | 0.2  | 5.0   |

| #4 | [m³] | [bar] |
|----|------|-------|
| A  | 0.0  | 0.0   |
| B  | 0.0  | 0.0   |


**A Total: 13.7 m³**
**B Total: 0.9 m³**
**Total: 14.7 m³**

Max. Volume [m³]

avg. Pressure [bar]

**6) Segments**
