



RING			POSITION OF THE CUTTERHEAD			EARTH PRESSURE BALANCE (EPB)			CH TORQUE			CH THRUST FORCE			GEOMETRICAL OF SOIL EXCAVATED			PRIMARY GROUT INJECTION		INJECTION OF FOAM				INJECTION OF BENTONITE		INJECTION OF WATER & BENTONITE		GEOMETRICAL OF MUCK EXTRACTED			PAT	
ID	Serial Number	Date of Installation	CH Initial [Km]	CH Final [Km]	Length [m]	Average Value [bar]	Min. Value [bar]	Max. Value [bar]	Average Value [MNm]	Min. Value [MNm]	Max. Value [MNm]	Average Value [kN]	Min. Value [kN]	Max. Value [kN]	Average Density [Ton/m³]	Volume (V1) [m³]	Weight (W1) [Ton]	Expected Backfill [m³]	Injected Backfill [m³]	Volume (V2) [m³]	Weight (W2) [Ton]	Volume (V3) [m³]	Weight (W3) [Ton]	Water (V4) [m3] = (W4) [Ton]	Volume (V5) [m³]	Weight (W5) [Ton]	(V6) [m3] = (W6) [Ton]	∑ _{i=1} ⁿ (V _i)	∑ _{i=1} ⁿ (W _i)	Density [Ton/m³]	Category of Soil	Description
(LWK-000-W-MG-INP-09-1003_00)																		1.230,39	1.421,08	1,1 [Ton/m³]		1,05 [Ton/m³]		2,55 [Ton/m³]								
101	D0895	28/07/2024	1*900,317	1*898,733	1,584	1,647	1,500	1,847	3,336	1,086	5,003	76.070	22.133	78.591	2,21	212,8	470,6	12,19	16,05	0,03	0,04	0,65	0,68	32,4	1,27	3,24	51,88	297,82	558,85	1,88	5% VIF 52% VIA 43% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
102	D1495	28/07/2024	1*898,721	1*897,089	1,633	1,617	1,515	1,787	2,321	0,731	5,191	79.888	23.291	85.122	2,21	219,4	484,7	12,56	14,14	0,21	0,23	0,91	0,96	46,3	1,61	4,09	65,51	332,31	601,82	1,81	5% VIF 49% VIA 46% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
103	D1539	28/07/2024	1*897,095	1*895,517	1,578	1,722	1,617	1,912	5,367	0,935	9,495	75.013	20.653	77.465	2,20	212,0	466,6	12,14	12,68	0,02	0,02	0,38	0,40	19,2	0,68	1,74	27,90	259,49	515,87	1,99	7% VIF 44% VIA 49% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
104	D1483	28/07/2024	1*895,511	1*893,907	1,604	1,742	1,643	1,890	6,491	2,055	12,908	72.818	18.047	75.631	2,19	215,5	472,4	12,34	12,87	0,00	0,00	0,50	0,52	25,1	0,88	2,24	35,84	276,91	536,13	1,94	9% VIF 39% VIA 52% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
105	D1766	28/07/2024	1*893,906	1*892,303	1,603	1,797	1,718	1,993	5,571	1,051	8,049	73.131	20.846	75.374	2,18	215,4	470,5	12,33	12,90	0,00	0,00	0,55	0,58	27,7	0,79	2,03	32,43	276,06	533,17	1,93	11% VIF 34% VIA 55% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
106	D1290	28/07/2024	1*892,303	1*890,712	1,592	1,767	1,689	1,877	5,375	0,981	8,196	76.909	17.854	79.653	2,18	213,9	465,3	12,25	12,50	0,00	0,00	0,50	0,52	24,9	0,87	2,22	35,50	274,76	528,41	1,92	13% VIF 29% VIA 58% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
107	D1047	28/07/2024	1*890,701	1*889,090	1,610	1,759	1,698	1,933	5,564	0,872	8,508	73.419	21.908	75.889	2,17	216,4	468,9	12,39	12,91	0,01	0,01	0,50	0,53	25,3	0,97	2,47	39,50	281,73	536,76	1,91	15% VIF 24% VIA 61% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
108	D1554	29/07/2024	1*889,091	1*887,510	1,581	1,749	1,591	1,931	5,863	1,274	8,560	73.596	20.717	77.015	2,16	212,4	458,5	12,16	15,20	0,00	0,00	0,57	0,60	28,6	0,87	2,21	35,39	276,97	525,29	1,90	17% VIF 19% VIA 64% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
109	D1567	29/07/2024	1*887,503	1*885,908	1,595	1,725	1,553	1,921	5,283	1,122	7,319	78.266	19.238	80.425	2,15	214,4	460,9	12,27	14,75	0,00	0,00	0,55	0,58	27,9	0,95	2,43	38,83	281,62	530,59	1,88	19% VIF 14% VIA 67% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
110	D0102	29/07/2024	1*885,904	1*884,364	1,540	1,766	1,683	1,987	3,703	0,996	6,576	86.832	24.546	90.751	2,14	207,0	443,3	11,85	13,05	0,10	0,11	0,93	0,98	46,8	1,14	2,91	46,49	301,29	540,53	1,79	21% VIF 9% VIA 70% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
111	D1570	30/07/2024	1*884,372	1*882,719	1,653	1,597	1,373	1,832	2,225	0,600	5,532	88.977	20.975	90.880	2,13	222,1	473,7	12,72	17,88	0,19	0,21	0,80	0,84	40,4	3,03	7,74	123,80	387,29	646,68	1,67	23% VIF 4% VIA 73% VIB	Sand and Silt Sands. Clay and Sandy Loam. Clay and Sandy Loam.
112	D1564	30/07/2024	1*882,728	1*880,978	1,750	1,630	1,311	1,896	2,203	0,512	5,102	88.656	19.527	94.772	2,13	235,1	500,4	13,46	13,99	0,60	0,66	1,05	1,10	52,4	2,38	6,06	97,01	386,21	657,62	1,70	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
113	D1429	31/07/2024	1*880,974	1*879,515	1,459	1,588	1,314	1,872	2,755	0,732	5,053	87.105	21.232	90.816	2,13	196,0	417,1	11,22	14,64	0,50	0,55	0,66	0,69	33,0	1,82	4,64	74,29	304,49	530,32	1,74	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
114	D1435	01/08/2024	1*879,507	1*877,911	1,596	1,539	1,051	1,814	3,048	0,771	5,177	84.604	19.302	89.979	2,13	214,4	456,3	12,28	19,26	0,72	0,79	0,65	0,68	58,2	1,74	4,44	70,99	345,02	591,44	1,71	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
115	D0322	01/08/2024	1*877,914	1*876,346	1,569	1,329	0,741	1,856	1,721	0,553	3,636	87.862	19.752	93.968	2,13	210,8	448,5	12,07	15,46	0,59	0,65	0,49	0,52	26,3	1,87	4,77	69,35	307,49	550,10	1,79	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
116	D1431	02/08/2024	1*876,345	1*874,713	1,633	1,420	0,927	1,957	1,130	0,460	4,165	86.129	19.398	94.612	2,13	219,4	466,8	12,56	21,53	1,20	1,32	2,03	2,13	123,9	4,89	12,48	181,49	528,01	788,16	1,49	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
117	D1432	02/08/2024	1*874,715	1*873,099	1,616	1,284	1,091	1,705	1,565	0,517	3,633	87.929	19.495	93.582	2,13	217,1	462,0	12,43	17,13	1,15	1,26	0,70	0,74	34,7	2,47	6,29	91,44	345,13	596,48	1,73	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
118	D1421	03/08/2024	1*873,096	1*871,536	1,560	1,206	1,011	1,650	2,042	0,635	4,359	82.862	24.385	88.564	2,13	209,7	446,2	12,01	15,92	0,61	0,67	0,66	0,69	33,5	1,58	4,04	58,77	303,22	543,87	1,79	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
119	D1422	03/08/2024	1*871,541	1*869,928	1,612	1,387	1,132	1,792	1,723	0,451	6,200	76.462	24.031	81.518	2,13	216,6	461,0	12,41	15,61	1,02	1,12	0,95	1,00	47,7	2,33	5,94	86,38	352,69	603,15	1,71	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
120	D1420	04/08/2024	1*869,928	1*868,329	1,599	1,440	1,204	1,840	2,656	0,550	6,594	79.804	23.098	84.317	2,13	214,9	457,3	12,30	14,75	0,75	0,83	0,55	0,58	28,0	1,81	4,60	66,96	311,16	558,26	1,79	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
121	D1430	04/08/2024	1*868,332	1*866,726	1,605	1,489	1,252	1,740	2,576	0,904	7,180	76.693	17.597	82.998	2,13	215,7	459,0	12,35	13,73	2,57	2,82	0,75	0,79	37,4	1,95	4,97	72,31	328,76	577,33	1,76	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
122	D1436	05/08/2024	1*866,716	1*865,117	1,599	1,654	1,245	1,934	3,361	0,914	7,568	73.931	4.986	77.819	2,13	214,9	457,4	12,31	16,12	1,13	1,24	0,76	0,80	39,4	2,30	5,85	85,14	341,39	589,83	1,73	24% VIF 76% VIB	Sand and Silt Sands. Clay and Sandy Loam.
123	D1577	06/08/2024	1*865,119	1*863,496	1,622	1,608	1,025	1,836	3,905	0,867	8,160	80.029	16.407	86.923	2,12	218,0	463,2	12,48	16,04	0,72	0,80	0,53	0,56	26,8	1,09	2,79	40,57	286,60	534,64	1,87	1% VIC 24% VIF 75% VIB	Sand and Silt Sands. Clay and Sandy Loam.
124	D1594	07/08/2024	1*863,499	1*861,918	1,581	1,628	1,499	1,947	4,766	1,664	9,196	75.894	22.615	80.972	2,12	212,5	450,7	12,17	14,44	0,41	0,45	0,52	0,55	26,3	1,37	3,49	50,73	290,43	532,20	1,83	2% VIC 24% VIF 74% VIB	Sand and Silt Sands. Clay and Sandy Loam.
125	D1583	07/08/2024	1*861,918	1*860,285	1,633	1,626	1,518	1,790	6,043	1,463	8,972	72.171	22.808	75.921	2,12	219,4	464,6	12,56	12,21	0,47	0,52	0,46	0,48	23,0	0,96	2,46	35,72	279,02	526,72	1,89	3% VIC 24% VIF 73% VIB	Sand and Silt Sands. Clay and Sandy Loam.
126	D1572	07/08/2024	1*860,273	1*858,685	1,588	1,613	1,506	1,787	7,005	1,118	9,103	69.613	19.141	73.219	2,11	213,3	451,0	12,21	12,24	0,46	0,51	0,43	0,45	21,9	1,03	2,62	38,05	274,17	514,49	1,88	4% VIC 24% VIF 73% VIB	Sand and Silt Sands. Clay and Sandy Loam.
127	D1051	07/08/2024	1*858,687	1*857,020	1,668	1,633	1,509	1,785	6,731	1,363	11,118	69.016	20.653	72.382	2,11	224,1	472,9	12,83	14,70	0,69	0,76	0,53	0,56	27,0	1,06	2,71	39,43	291,69	543,33	1,86	5% VIC 24% VIF 73% VIB	Sand and Silt Sands. Clay and Sandy Loam.
128	D1084	07/08/2024	1*857,021	1*855,471	1,550	1,640	1,537	1,869	6,700	1,165	9,449	70.348	23.967	73.830	2,11	208,2	438,7	11,92	13,73	0,51	0,56	0,40	0,42	20,2	1,12	2,85	41,53	270,86	504,28	1,86	6% VIC 24% VIF 73% VIB	Sand and Silt Sands. Clay and Sandy Loam.
129	D1089	08/08/2024	1*855,471	1*853,688	1,783	1,636	1,541	1,822	7,745	1,056	11,196	70.176	22.004	73.798	2,10	239,6	504,1	13,72	16,31	0,75	0,82	0,49	0,51	25,0	0,16	0,40	5,81	271,67	536,62	1,98	7% VIC 24% VIF 73% VIB	Sand and Silt Sands. Clay and Sandy Loam.
130	D1166	08/08/2024	1*853,688	1*852,273	1,415	1,602	1,504	1,885	8,899	1,265	11,861	72.894	17.919	76.018	2,10	190,2	399,4	10,89	11,99	0,44	0,48	0,41	0,43	20,9	0,85	2,18	38,73	250,61	462,05	1,84	8% VIC 24% VIF 73% VIB	Sand and Silt Sands. Clay and Sandy Loam.
131	0	08/08/2024	1*852,269	1*850,670	1,599	1,489	1,428	1,641	7,274	0,956	9,682	70.933	20.203	75.052	2,10	214,8	450,4	12,30	11,93	0,75	0,82	0,47	0,49	23,4	0,60	1,54	27,42	266,90	504,09	1,89	9% VIC 24% VIF 73% VIB	Sand and Silt Sands. Clay and Sandy Loam.
132	0	08/08/2024	1*850,668	1*849,049	1,620	1,508	1,401	1,832	9,284	1,108	13,205	68.817	22.036	73.090	2,09	217,6	455,5	12,46	13,28	0,86	0,94	0,44	0,46	22,1	0,41	1,06	18,80	259,80	498,81	1,92	10% VIC 24% VIF 73% VIB	Sand and Silt Sands. Clay and Sandy Loam.
133	0	08/08/2024	1*849,047	1*847,421	1,626	1,591	1,375																									

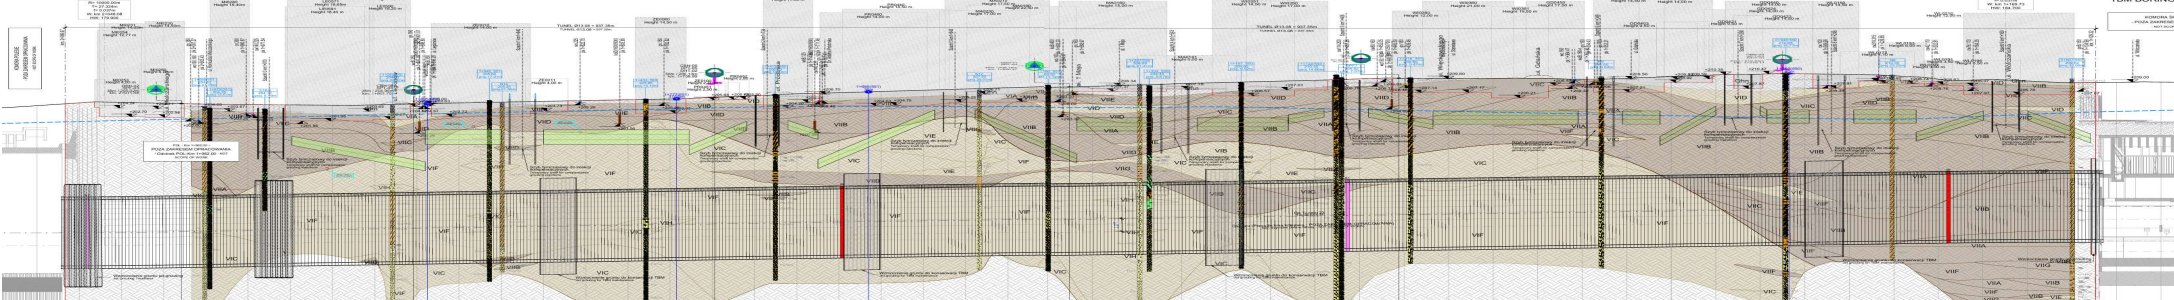

RING			POSITION OF THE CUTTERHEAD			EARTH PRESSURE BALANCE (EPB)			CH TORQUE			CH THRUST FORCE			GEOMETRICAL OF SOIL EXCAVATED			PRIMARY GROUT INJECTION		INJECTION OF FOAM					INJECTION OF BENTONITE			GEOMETRICAL OF MUCK EXTRACTED			PAT	
ID	Serial Number	Date of Installation	CH Initial [Km]	CH final [Km]	Length [m]	Average Value [bar]	Min. Value [bar]	Max. Value [bar]	Average Value [MNm]	Min. Value [MNm]	Max. Value [MNm]	Average Value [kN]	Min. Value [kN]	Max. Value [kN]	Average Density [Ton/m³]	Volume (V1) [m³]	Weight (W1) [Ton]	Expected Backfill [m³]	Injected Backfill [m³]	Volume (V2) [m³]	Weight (W2) [Ton]	Volume (V3) [m³]	Weight (W3) [Ton]	(V4) [m3] = (W4) [Ton]	Volume (V5) [m³]	Weight (W5) [Ton]	(V6) [m3] = (W6) [Ton]	$\sum_{i=1}^5 (V_i)$	$\sum_{i=1}^6 (W_i)$	Density [Ton/m³]	Category of Soil	TUNNEL AXIS 23 (POL-SRD)
(LWK-000-W-MG-INP-09-1003_00)																		1.230,39	1.421,08	1,1	[Ton/m³]	1,05	[Ton/m³]	2,55	[Ton/m³]							
156	0	13/08/2024	1+812,216	1+810,589	1,627	1,613	1,381	1,883	6,210	0,883	10,985	69,363	22,776	73,476	1,88	218,7	411,0	12,52	13,74	0,18	0,20	0,50	0,52	20,6	0,63	1,60	28,40	268,40	462,33	1,72	2% VC 65% VIC 29% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
157	D1419	13/08/2024	1+810,582	1+809,011	1,571	1,655	1,497	1,947	6,643	0,889	15,814	70,466	23,838	73,991	1,88	211,1	396,5	12,08	13,89	0,16	0,17	0,36	0,38	16,5	0,57	1,46	26,04	254,14	441,11	1,74	2% VC 66% VIC 28% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
158	D1372	13/08/2024	1+809,009	1+807,407	1,602	1,660	1,461	1,893	9,066	1,531	14,764	64,231	17,340	68,554	1,88	215,2	404,2	12,32	13,07	0,07	0,08	0,37	0,39	16,0	0,59	1,50	26,72	258,34	448,89	1,74	2% VC 67% VIC 27% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
159	D1815	13/08/2024	1+807,407	1+805,791	1,616	1,628	1,516	1,790	7,111	1,025	15,344	67,251	19,109	70,291	1,88	217,1	407,7	12,43	15,32	0,06	0,07	0,43	0,46	18,3	0,64	1,64	29,15	265,07	457,33	1,73	2% VC 68% VIC 26% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
160	0	14/08/2024	1+805,788	1+804,211	1,577	1,625	1,428	1,863	3,665	0,688	6,062	73,056	22,712	78,430	1,88	211,9	397,8	12,13	13,95	0,02	0,03	0,49	0,52	18,5	0,78	1,98	35,21	266,10	454,01	1,71	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
161	0	14/08/2024	1+804,197	1+802,612	1,585	1,568	1,388	1,704	5,891	0,966	12,835	78,069	20,685	83,964	1,88	212,9	399,7	12,19	13,91	0,09	0,10	0,39	0,41	14,5	0,79	2,02	35,88	263,83	452,68	1,72	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
162	0	15/08/2024	1+802,609	1+801,028	1,581	1,590	1,291	1,962	5,581	0,812	12,790	81,997	23,806	91,362	1,88	212,5	398,9	12,17	19,63	0,22	0,24	0,42	0,44	16,0	1,71	4,36	77,49	306,56	497,37	1,62	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
163	0	15/08/2024	1+801,013	1+799,395	1,618	1,576	1,438	1,744	5,007	0,834	8,114	84,839	21,136	88,596	1,88	217,4	408,2	12,45	12,27	0,27	0,30	0,37	0,39	13,8	0,60	1,52	27,00	258,91	451,23	1,74	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
164	0	15/08/2024	1+799,395	1+797,824	1,570	1,535	1,328	1,681	6,850	0,778	15,422	8,466	23,902	87,084	1,88	211,0	396,1	12,08	11,33	0,21	0,23	0,35	0,37	13,1	0,66	1,69	29,99	254,69	441,54	1,73	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
165	D1590	15/08/2024	1+797,824	1+796,204	1,620	1,638	1,459	1,888	4,328	0,743	7,915	82,892	26,218	86,505	1,88	217,7	408,7	12,47	15,38	0,26	0,29	0,51	0,53	18,9	0,92	2,34	41,53	278,96	472,34	1,69	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
166	D1427	15/08/2024	1+796,202	1+794,592	1,610	1,627	1,487	1,881	7,032	1,076	10,213	79,795	24,514	84,736	1,88	216,3	406,1	12,39	14,64	0,12	0,14	0,44	0,46	16,5	0,78	2,00	32,02	265,45	457,27	1,72	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
167	0	16/08/2024	1+794,588	1+792,984	1,603	1,614	1,446	1,951	5,468	1,049	8,518	76,471	25,639	81,261	1,88	215,4	404,4	12,34	15,01	0,27	0,29	0,62	0,65	24,5	1,00	2,54	40,71	281,54	473,14	1,68	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
168	0	16/08/2024	1+792,979	1+791,382	1,596	1,598	1,125	1,771	5,263	0,818	8,055	74,887	24,578	80,746	1,88	214,5	402,6	12,28	13,87	0,31	0,34	0,36	0,38	14,5	0,66	1,68	26,87	256,48	446,36	1,74	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
169	0	16/08/2024	1+791,383	1+789,784	1,598	1,662	1,371	1,887	5,987	0,882	9,988	73,765	20,621	77,369	1,88	214,8	403,2	12,30	13,26	0,19	0,21	0,37	0,39	14,8	0,68	1,72	27,58	257,75	447,94	1,74	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
170	0	16/08/2024	1+789,778	1+788,176	1,602	1,665	1,489	1,877	6,740	0,837	10,723	75,042	18,723	78,430	1,88	215,3	404,2	12,33	13,62	0,19	0,21	0,40	0,42	16,1	0,65	1,66	26,49	258,50	449,07	1,74	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
171	0	16/08/2024	1+788,177	1+786,568	1,609	1,600	1,452	1,736	6,735	0,859	10,434	79,646	18,755	82,838	1,88	216,1	405,8	12,38	15,05	0,26	0,29	0,48	0,50	19,1	0,65	1,67	26,68	262,69	454,03	1,73	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
172	0	16/08/2024	1+786,566	1+784,984	1,581	1,598	1,487	1,850	5,308	0,953	9,520	80,679	21,457	86,505	1,88	212,5	398,9	12,17	13,50	0,20	0,22	0,50	0,53	23,5	0,89	2,26	36,18	272,84	461,55	1,69	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
173	0	17/08/2024	1+784,980	1+783,367	1,613	1,610	1,405	1,843	5,632	0,898	9,142	84,259	24,224	88,435	1,88	216,7	406,9	12,41	15,38	0,22	0,24	0,48	0,50	23,4	1,37	3,49	55,83	296,68	490,37	1,65	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
174	0	17/08/2024	1+783,363	1+781,769	1,594	1,632	1,448	1,831	7,327	0,926	11,142	85,042	25,639	88,210	1,88	214,1	402,0	12,26	12,82	0,19	0,20	0,34	0,35	14,1	0,69	1,76	28,20	257,00	446,66	1,74	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
175	0	17/08/2024	1+781,756	1+779,331	2,424	1,598	1,461	1,752	7,730	0,916	11,626	79,487	27,216	83,417	1,88	325,7	611,5	18,65	14,81	0,22	0,25	0,35	0,37	14,0	0,37	0,93	14,95	355,31	642,05	1,81	2% VC 69% VIC 25% VIF 4% VIIB	Clay and Silt Clay. Sand and Silt Sands. Sand and Silt Sands. Clay and Sandy Loam.
176	0	17/08/2024	1+779,332	1+778,570	0,762	1,641	1,504	1,835	8,836																							

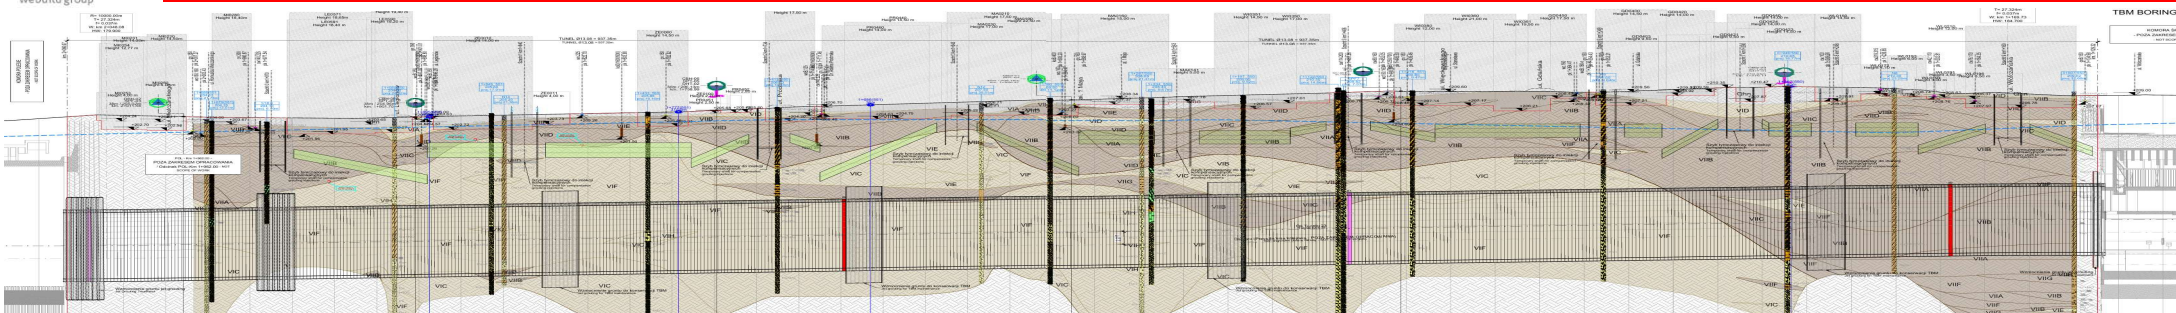

RING			POSITION OF THE CUTTERHEAD			EARTH PRESSURE BALANCE (EPB)			CH TORQUE			CH THRUST FORCE			GEOMETRICAL OF SOIL EXCAVATED			PRIMARY GROUT INJECTION		INJECTION OF FOAM					INJECTION OF BENTONITE				GEOMETRICAL OF MUCK EXTRACTED			PAT		
ID	Serial Number	Date of Installation	CH Initial [Km]	CH final [Km]	Length [m]	Average Value [bar]	Min. Value [bar]	Max. Value [bar]	Average Value [MNm]	Min. Value [MNm]	Max. Value [MNm]	Average Value [kN]	Min. Value [kN]	Max. Value [kN]	Average Density [Ton/m³]	Volume (V1) [m³]	Weight (W1) [Ton]	Expected Backfill [m³]	Injected Backfill [m³]	POLYMER		SURFACTANT		WATER		BENTONITE		WATER & BENTONITE		THEORETICAL OF CONDITIONED SOIL			Category	Description
(LWK-000-W-MG-INP-09-1003_00)																		1.230,39	1.421,08	1.1	[Ton/m³]	1.05	[Ton/m³]	2.55	[Ton/m³]	$\sum_{i=1}^n (V_i)$	$\sum_{i=1}^n (W_i)$	Density [Ton/m³]						
200	D1337	22/08/2024	1+741,743	1+740,135	1,608	1,632	1,472	1,835	8,467	1,629	11,776	63.618	19.077	67.364	1,90	216,1	410,7	12,37	12,93	0,31	0,34	0,38	0,40	19,3	0,70	1,78	35,65	271,80	468,26	1,72	2% VB 2% VC 96% VIF	Clay and Silt Clay. Clay and Silt Clay. Sand and Silt Sands.		
